ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		Busqueda de IA	1,13 days	Tue 11/11/25	Tue 11/11/25	
2		Investigación de lenguaje(Dani)	3 days	Wed 12/11/25	Thu 13/11/25	
3		Informe IA's	5 days	Thu 13/11/25	Mon 24/11/21	
4		Investigación de lenguaje(Sofi)	3 days	Fri 14/11/25	Sun 16/11/25	
5		Investigación de lenguaje(Adri)	3 days	Wed 12/11/25	Wed 19/11/25	
6		Investigación de lenguaje(Anai)	3 days	Wed 12/11/25	Thu 13/11/25	
7		Reunión	1 day	Fri 07/11/25	Fri 07/11/25	
8		Reunion	1 day	Sun 09/11/25	Sun 09/11/25	
9		Especificaciones del proyecto	1 day	Wed 08/10/25	Wed 08/10/25	
10		Especificaciones del proyecto	1 day	Tue 14/10/25	Tue 14/10/25	
11		Especificaciones del proyecto	1 day	Fri 17/10/25	Fri 17/10/25	
12		Especificaciones del proyecto	1 day	Tue 04/11/25	Tue 04/11/25	
13		Especificaciones del proyecto	1 day	Fri 07/11/25	Fri 07/11/25	
14		Diagrama de Gantt v1	0 days	Sun 09/11/25	Sun 09/11/25	
15		Redacción v1 Manual	1 day	Mon 20/10/2	Mon 20/10/2	
16		Redacción Manual v2	1 day	Tue 21/10/25	Tue 21/10/25	

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
17			Redacción Manual v3	1 day	Mon 10/11/2	Mon 10/11/2	
18			Busqueda web para Gantt v2	1 day	Mon 10/11/25	Mon 10/11/25	
19			Busqueda web para Gantt v2	1 day	Tue 11/11/25	Tue 11/11/25	
20			Diagrama de Gantt v2	4 days	Tue 11/11/25	Fri 14/11/25	
21			Creación de la estructura de BD	2 days	Thu 13/11/25	Fri 14/11/25	2
22			Pantalla de carga	1 day	Sun 16/11/25	Sun 16/11/25	21;6
23			Pantalla de Iniciar sesión	1 day	Sun 16/11/25	Sun 16/11/25	21;6
24			Pantalla de registro	1 day	Sun 16/11/25	Sun 16/11/25	21;6
25			Pantalla de recuperar	1 day?	Sun 16/11/25	Sun 16/11/25	21;6
26			Validación de datos de las pantallas	2 days	Sun 16/11/25	Mon 17/11/25	22;23;24;25
27			Crear pantalla de datos de usuario	3 days	Wed 19/11/25	Thu 20/11/25	4
28			Crear la base de dato	3 days	Wed 19/11/2	Tue 25/11/25	5
29			Función para registrar un usuario	2 days	Thu 20/11/25	Fri 21/11/25	24
30			Función para Iniciar sesión	2 days	Mon 17/11/25	Sat 22/11/25	23
31			Función para cerrar sesión	2 days	Sun 23/11/25	Tue 25/11/25	30

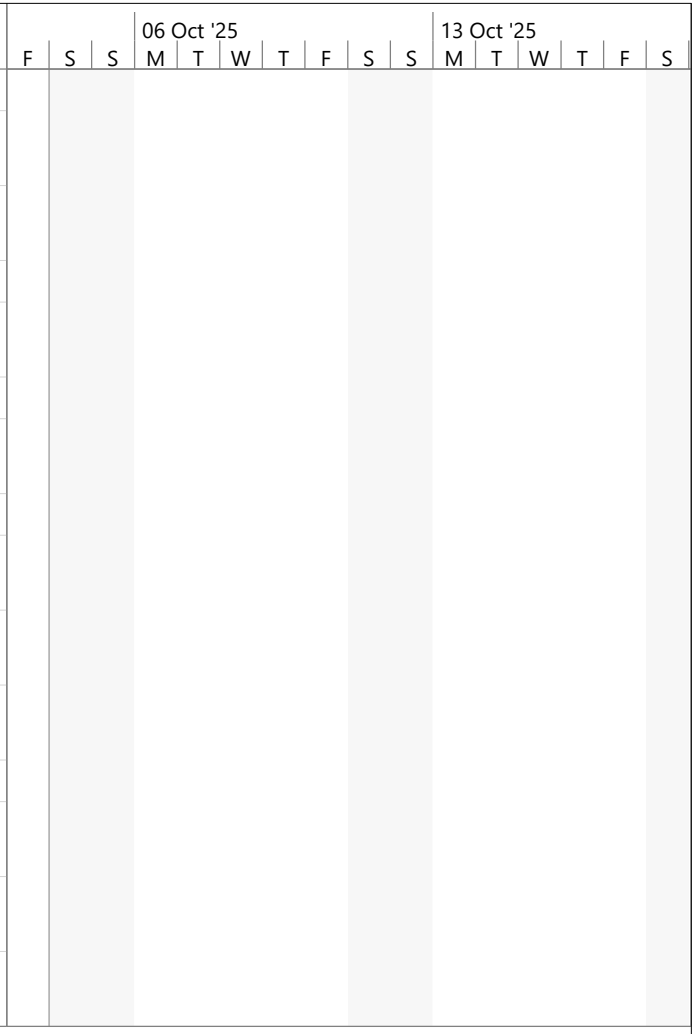

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
32			Función para guardar el inicio de sesión	2 days	Sat 22/11/25	Sun 23/11/25	30
33			Pantalla de selección de perfil	3 days	Tue 18/11/25	Sat 22/11/25	4
34			Guardar datos de usuario en la BD	2 days	Thu 20/11/25	Sun 23/11/25	27
35			Guardar los datos del perfil en la BD	2 days	Mon 24/11/25	Wed 26/11/25	33;36
36			Pantalla de preferencias de	3 days	Sat 22/11/25	Mon 24/11/25	4
37			Pantalla de inicio sin datos	3 days	Sat 15/11/25	Wed 19/11/25	6
38			Mostrar información inicial	2 days	Tue 25/11/25	Thu 27/11/25	37
39			Pantalla de inicio con datos guardados	3 days	Mon 24/11/25	Tue 25/11/25	4
40			Mostrar información pantalla de inicio con datos	1 day?	Tue 25/11/25	Wed 26/11/25	39
41			Pantalla de buscar recetas	3 days	Wed 19/11/25	Fri 21/11/25	6
42			Acceder a la cámara y enviar foto de los ingredientes a la IA	2 days	Thu 27/11/25	Fri 28/11/25	41

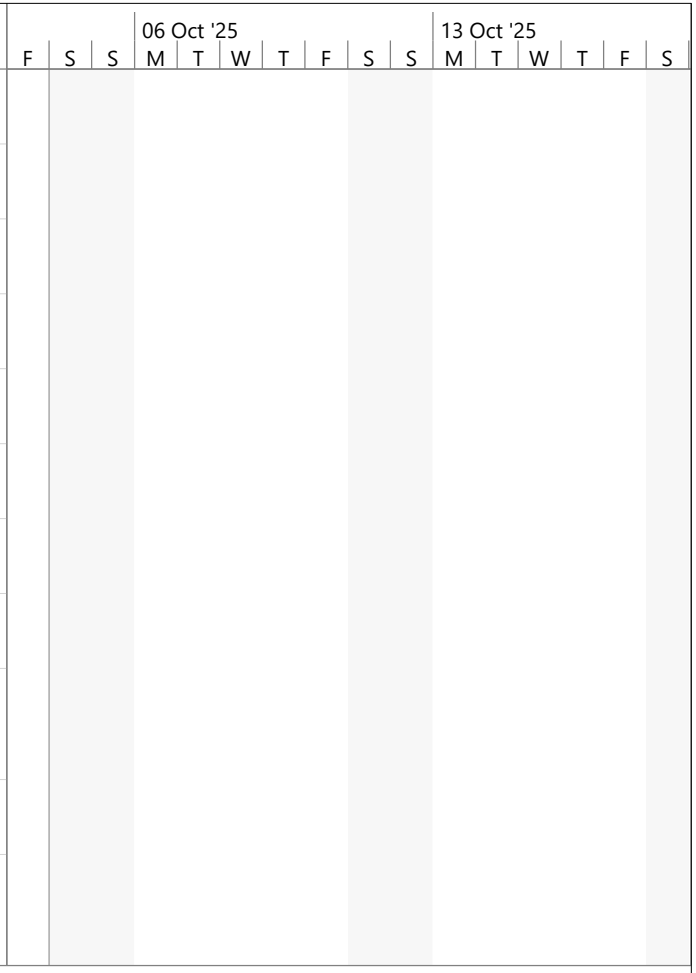

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
43			Buscar recetas por texto o palabra clave (IA).	2 days	Fri 28/11/25	Sat 29/11/25	41
44			Buscar recetas dinámicamente según los ingredientes	2 days	Sat 29/11/25	Sun 30/11/25	41
45			Ver una receta a deta	3 days	Wed 26/11/2	Thu 27/11/25	4
46			Enviar y guardar dato	3 days	Thu 27/11/25	Mon 01/12/2	45
47			Crear Receta Personalizada	2 days	Mon 17/11/25	Sat 22/11/25	4
48			Guardar datos de receta personalizada en la BD	2 days	Sun 30/11/25	Mon 01/12/25	47
49			Editar una receta personalizada	3 days	Tue 25/11/25	Sat 29/11/25	4
50			Funcion para editar receta	2 days	Sat 29/11/25	Sun 30/11/25	49
51			Recetas guardadas	3 days	Sat 22/11/25	Sun 23/11/25	6
52			Función que llame a la BBDD y devuelva un listado con todas las recetas del perfil	2 days	Mon 01/12/25	Wed 03/12/25	51
53			Función para guardar y flitrar las recetas favoritas del usuario.	2 days	Wed 03/12/25	Thu 04/12/25	51

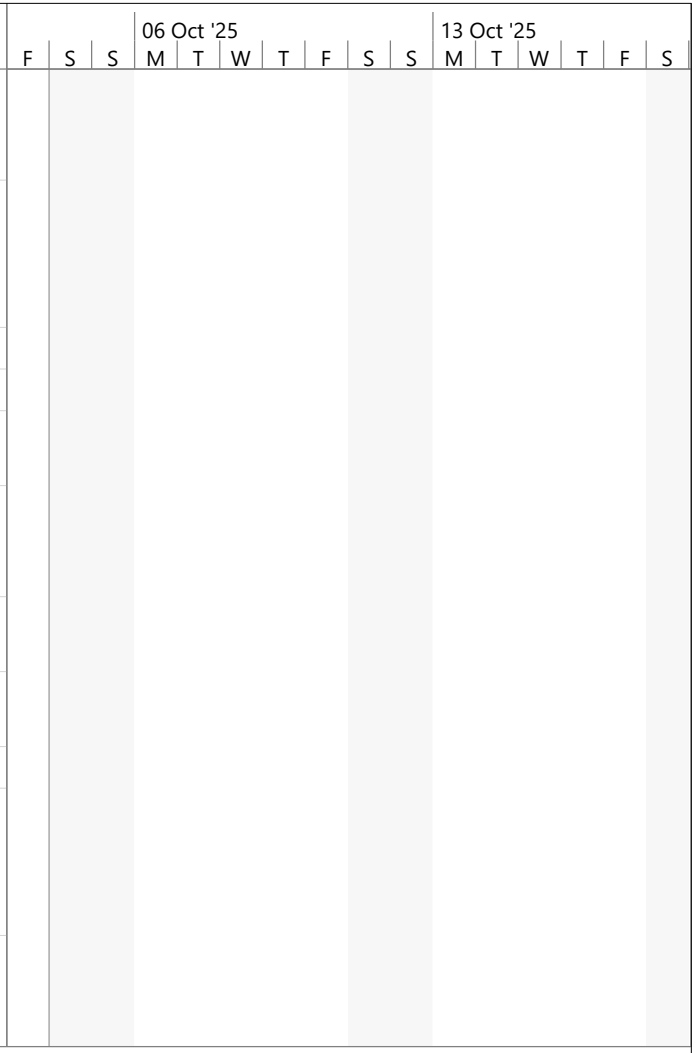

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
54			Añadir comida extra	3 days	Sat 29/11/25	Mon 01/12/24	
55			Añadir comida extra al calórico y a la lista diaria de extras.	2 days	Mon 01/12/25	Tue 02/12/25	54
56			Planificación de comidas (menú semanal)	3 days	Thu 13/11/25	Sat 15/11/25	6
57			Funciones de menú	3 days	Sat 15/11/25	Mon 17/11/25	56
58			Lista de la compra	3 days	Mon 01/12/2	Wed 03/12/24	
59			Función que, a partir del menú del usuario, genera la lista con los	2 days	Sat 06/12/25	Sun 07/12/25	58
60			Funciones para guardar, editar y eliminar listas de	2 days	Thu 04/12/25	Sat 06/12/25	58
61			Planificación de eventos (opcional)	4 days	Sun 07/12/25	Wed 14/01/26	1;22;23;24;25;26;
62			Función para generar el menú del evento ajustando las cantidades de los ingredientes.	3 days	Wed 14/01/26	Sun 18/01/26	61

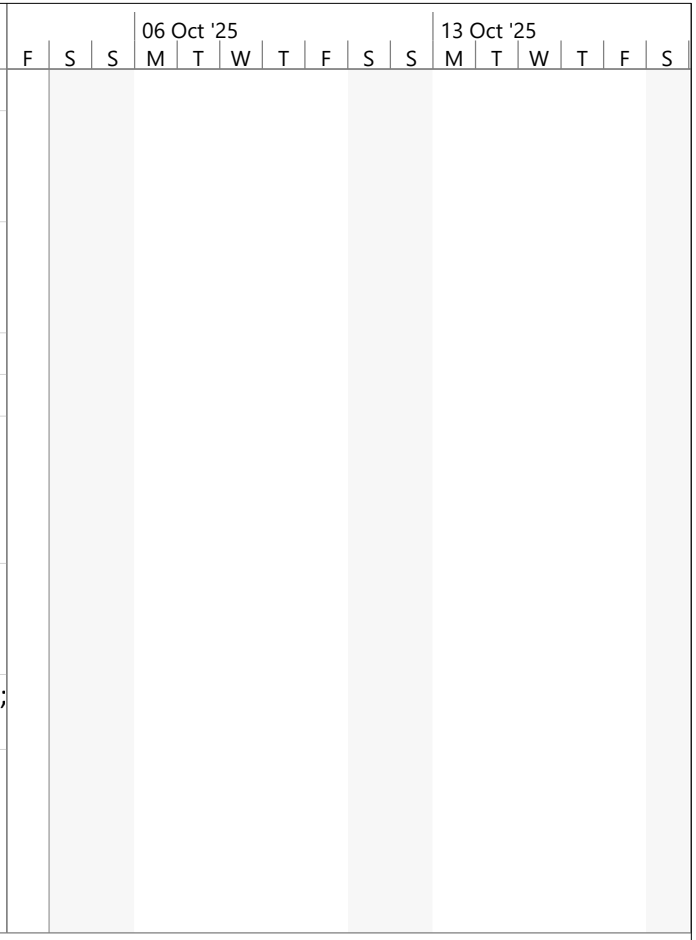

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
63			Función para detectar ingredientes perjudiciales para cualquiera de los	3 days	Wed 14/01/26	Fri 16/01/26	61
64			Ajustes y configuracić	4 days	Sun 16/11/25	Tue 18/11/25	4
65			Guardar los cambios en la base de datos.	2 days	Fri 21/11/25	Sat 22/11/25	64
66			Permitir actualizar las configuraciones del usuario.	3 days	Tue 18/11/25	Thu 20/11/25	64
67			Documentación	107 days	Sat 04/10/25	Sat 28/02/26	
68			Test	52 days	Tue 09/12/25	Wed 18/02/26	63

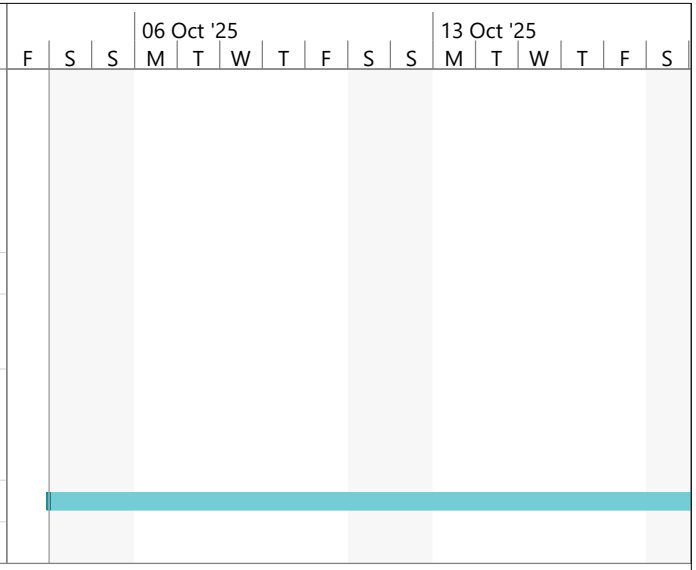

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

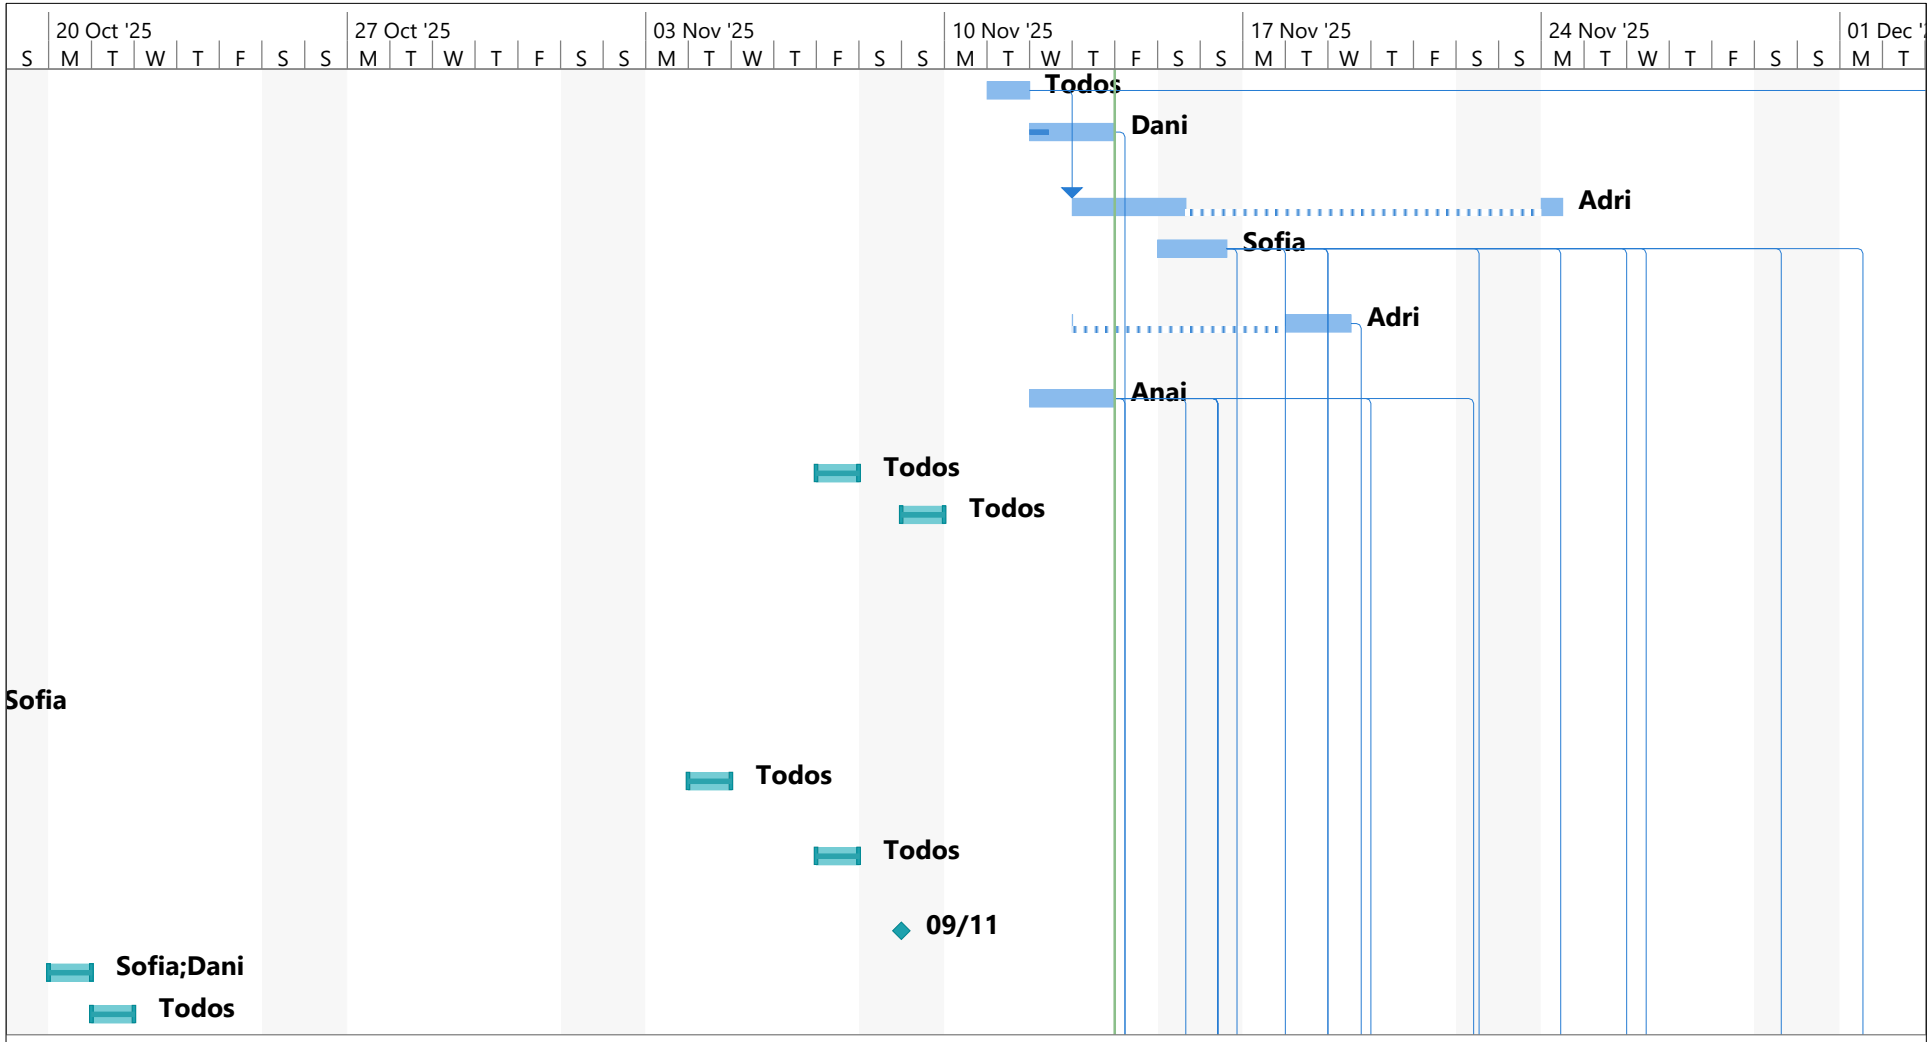

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

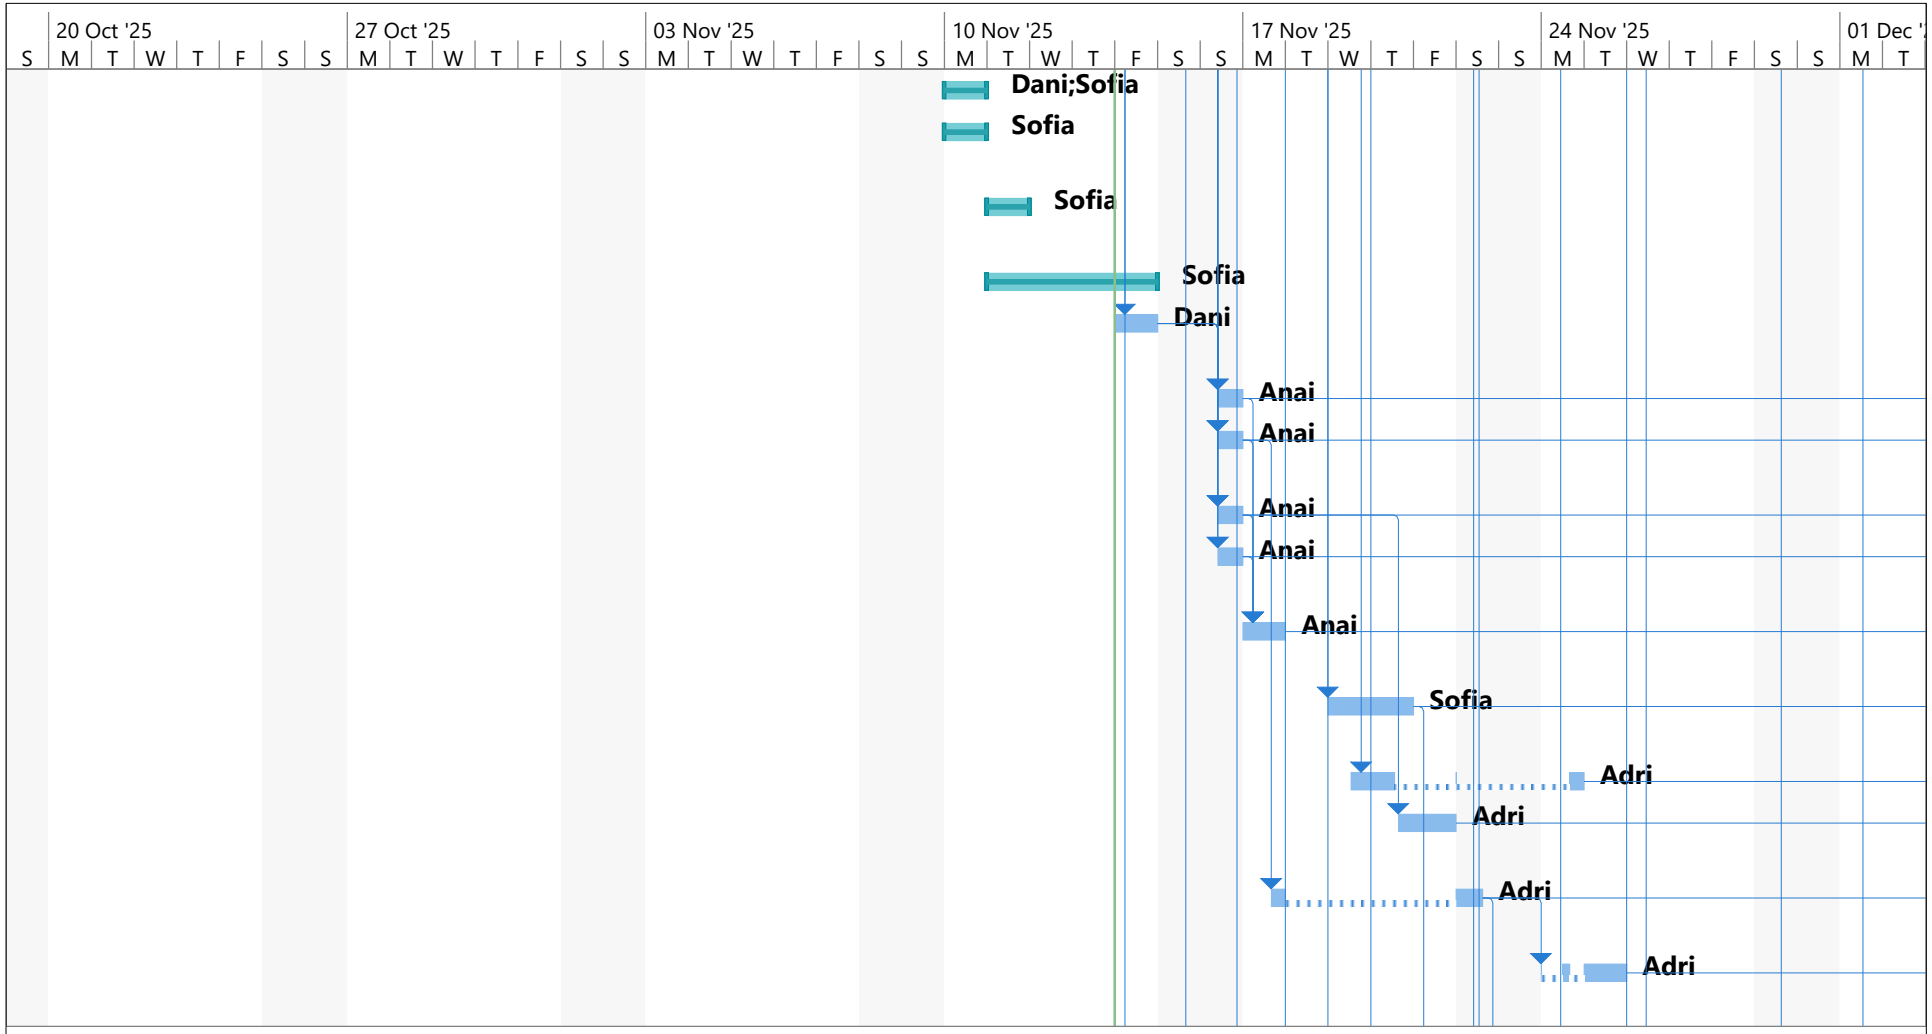

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

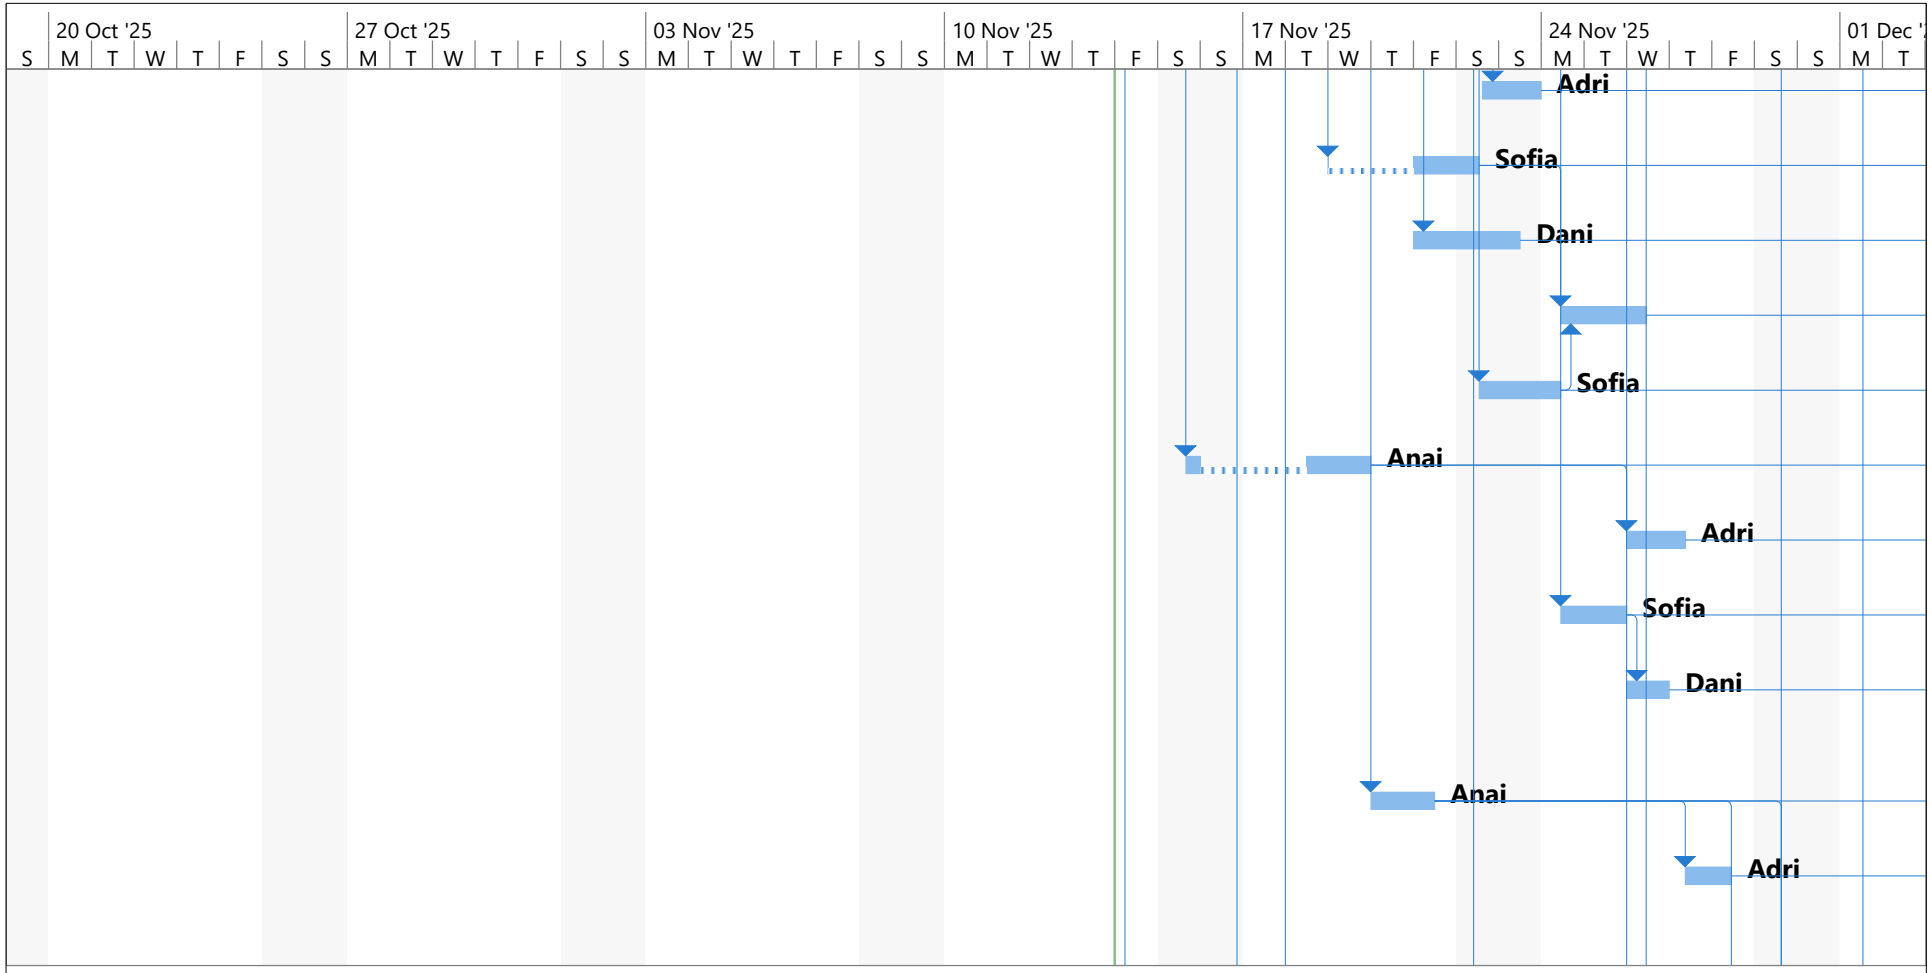

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

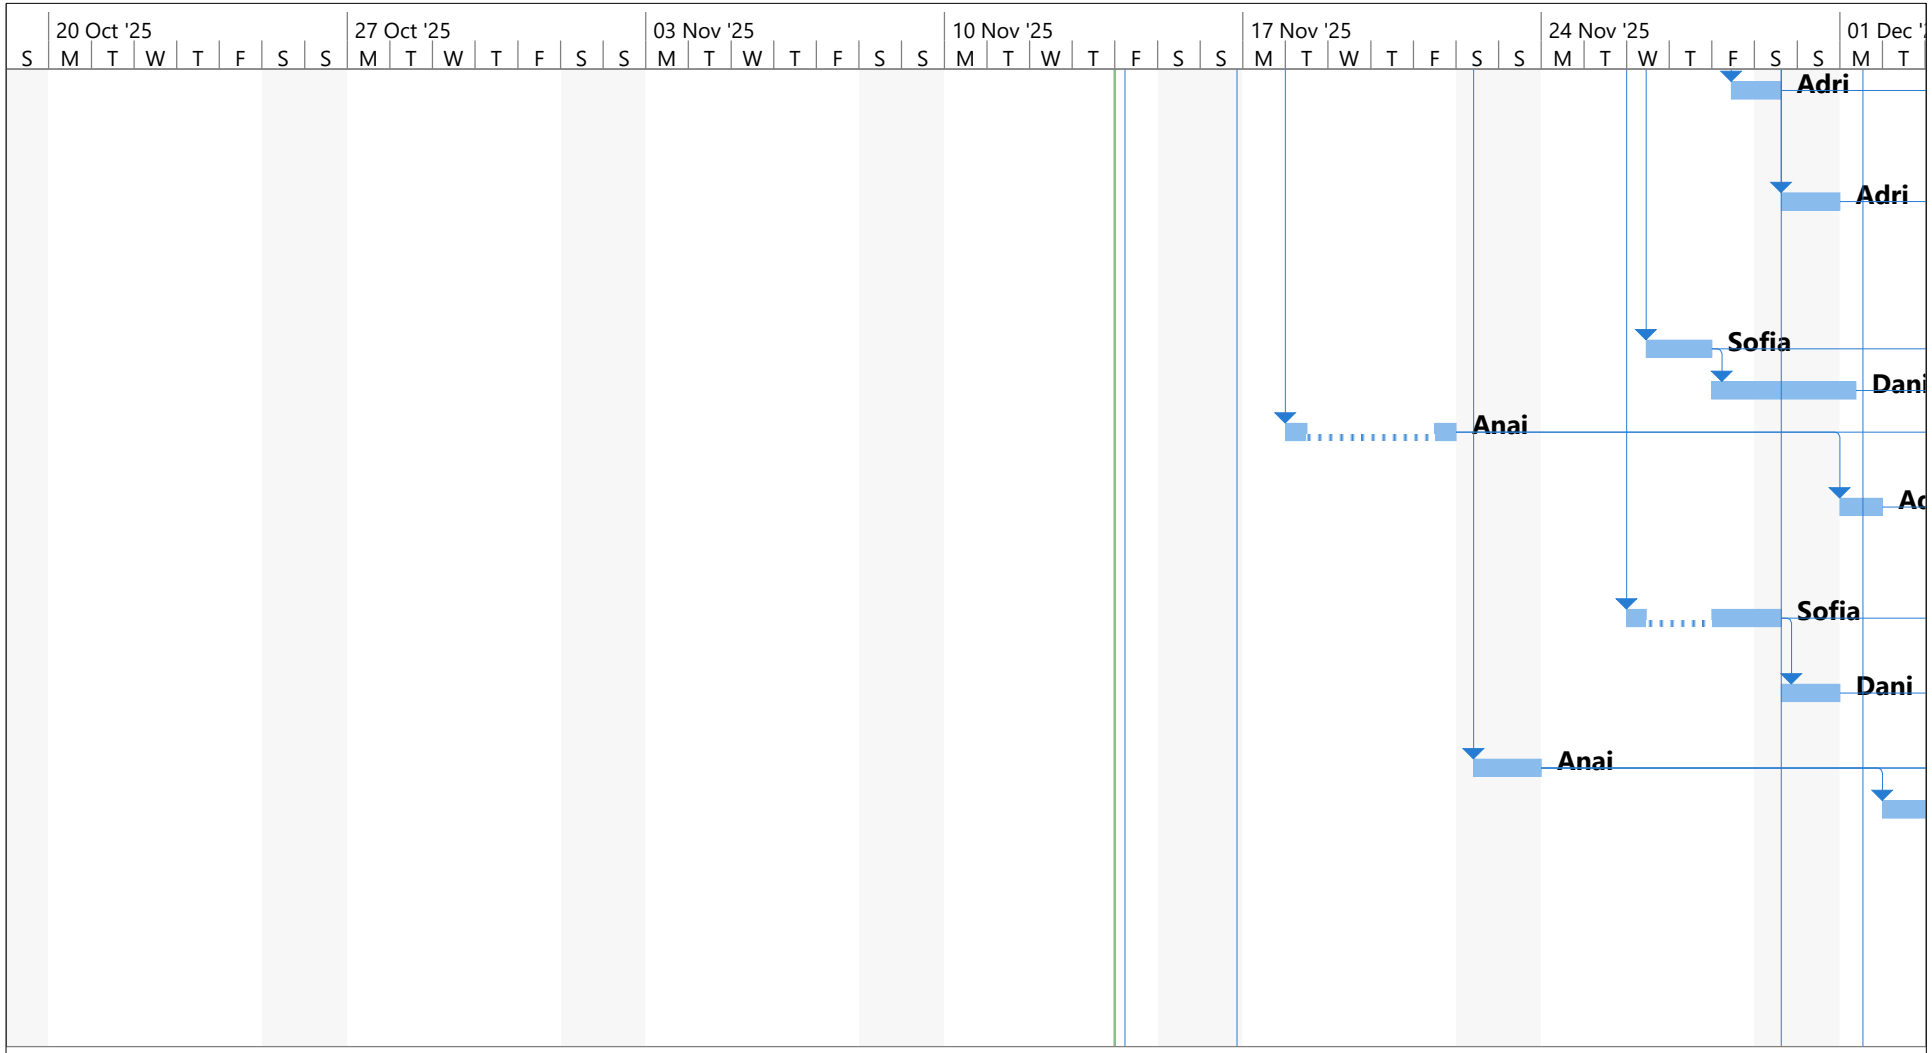

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

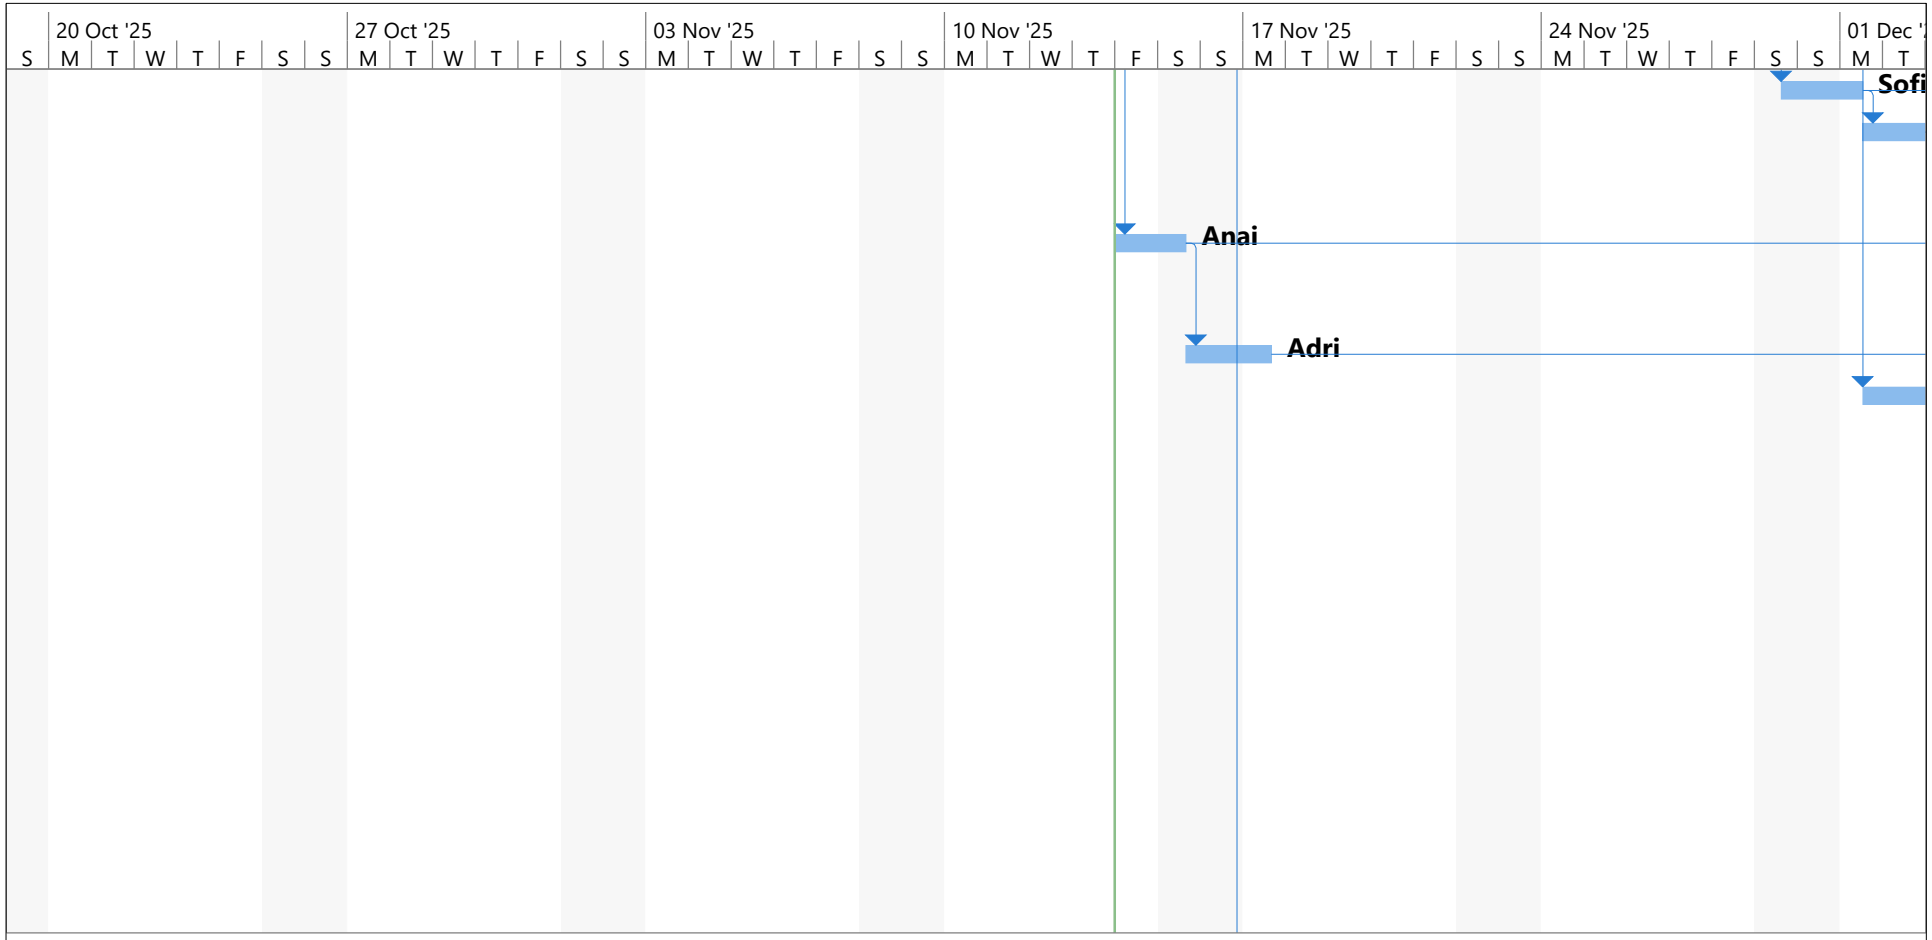

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

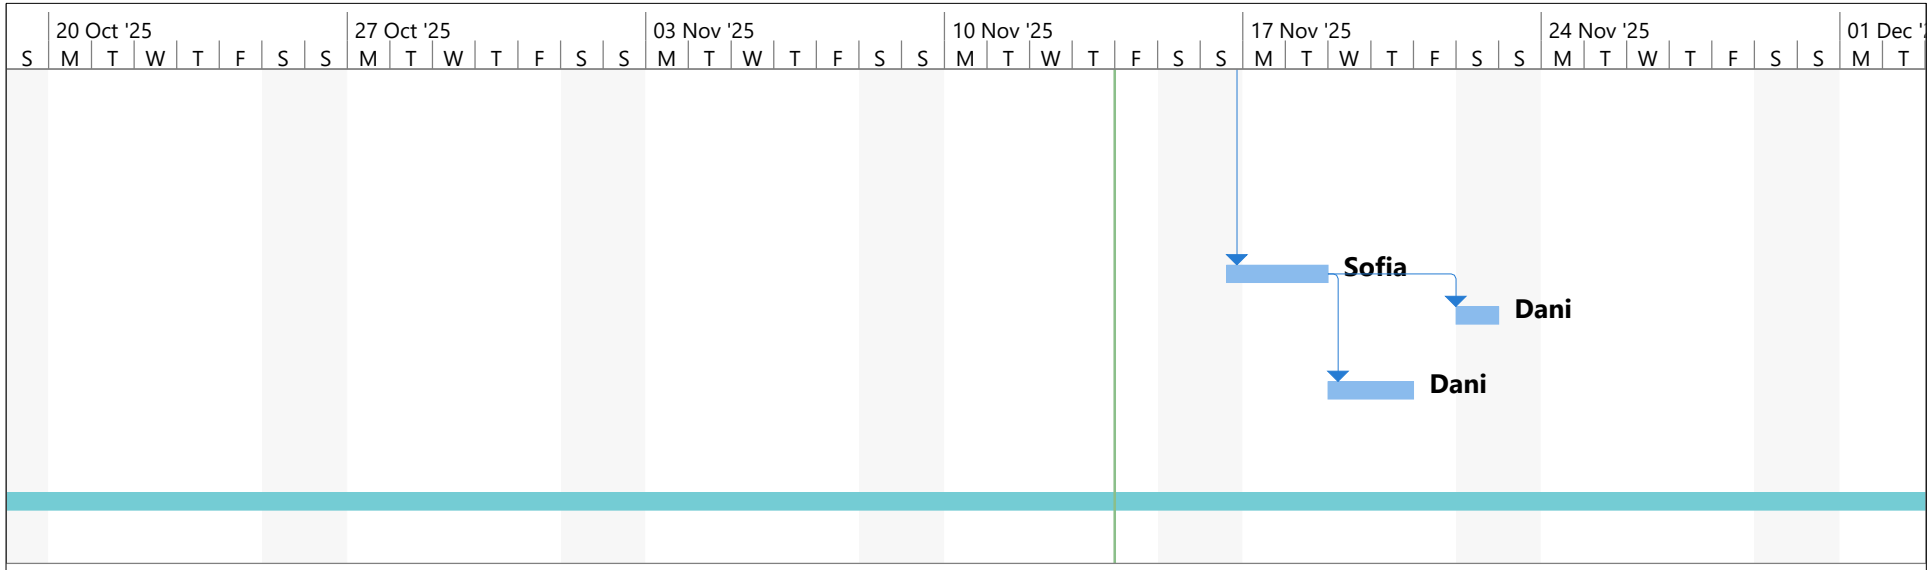

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

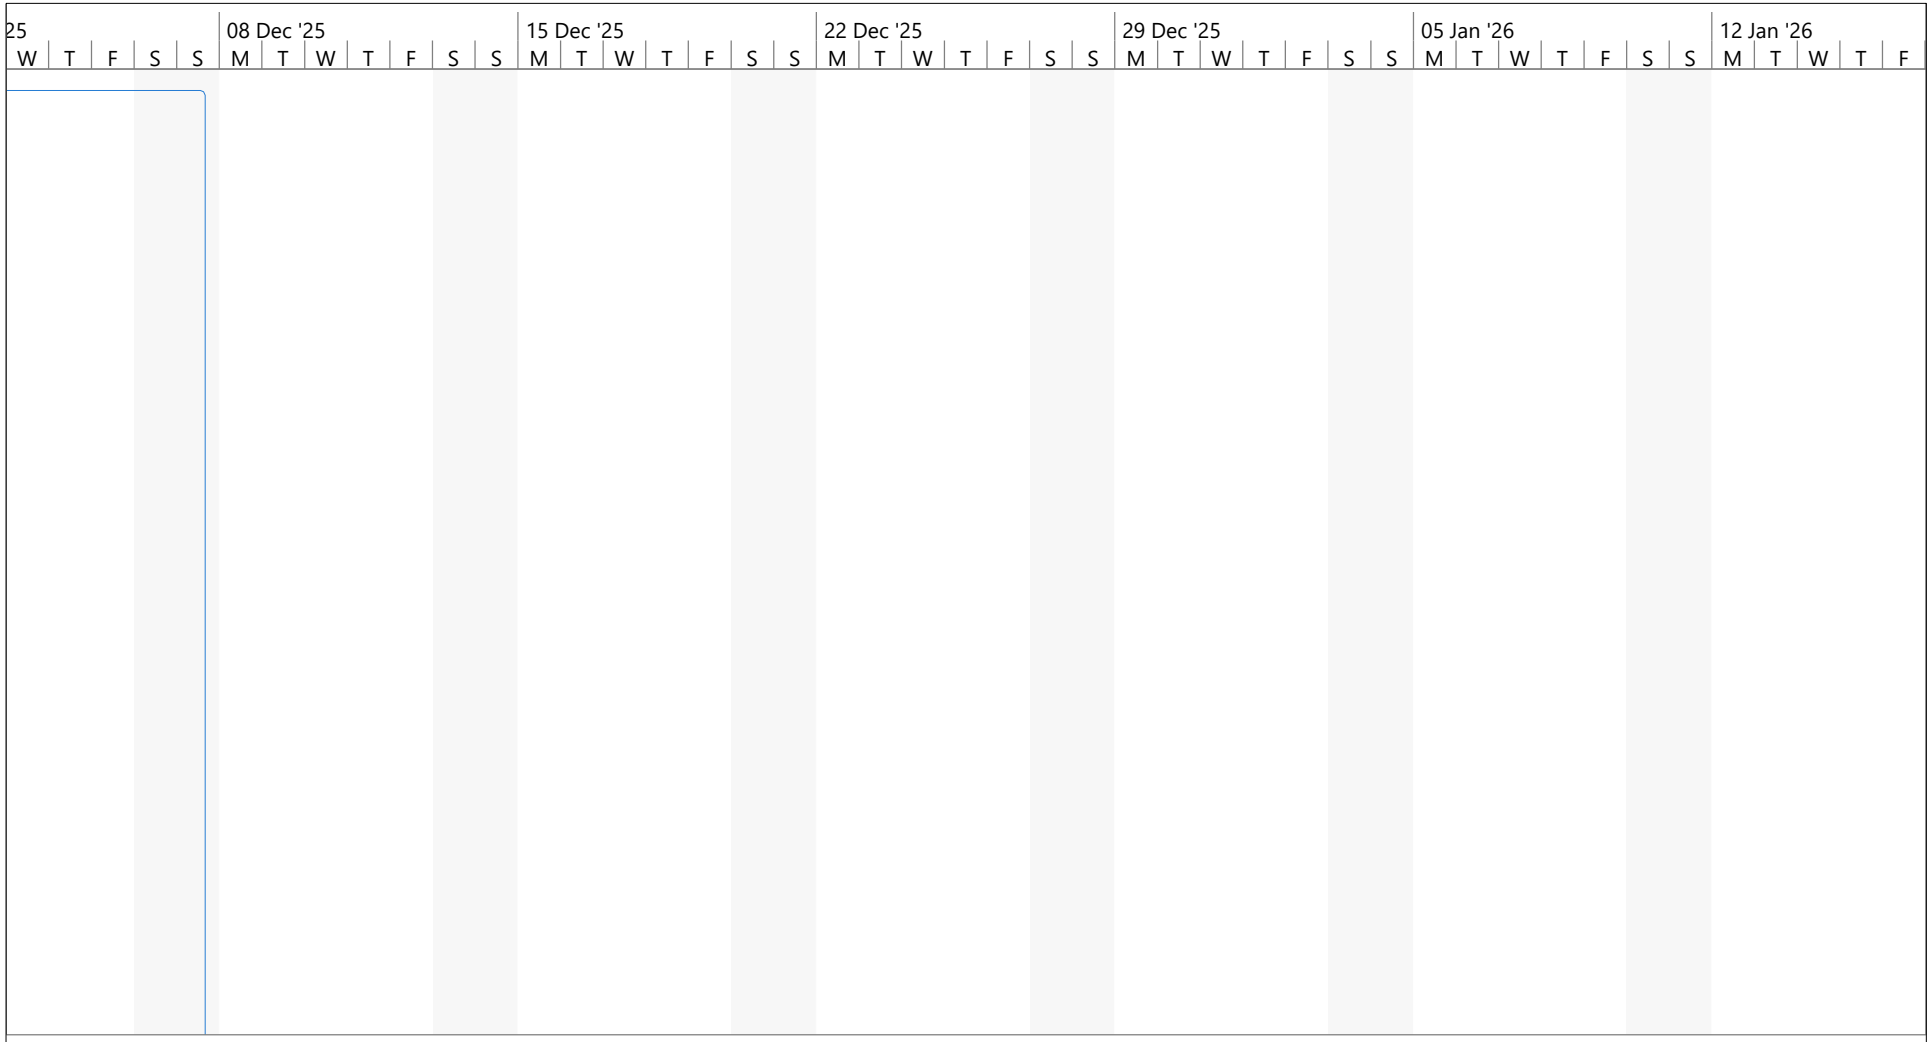

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

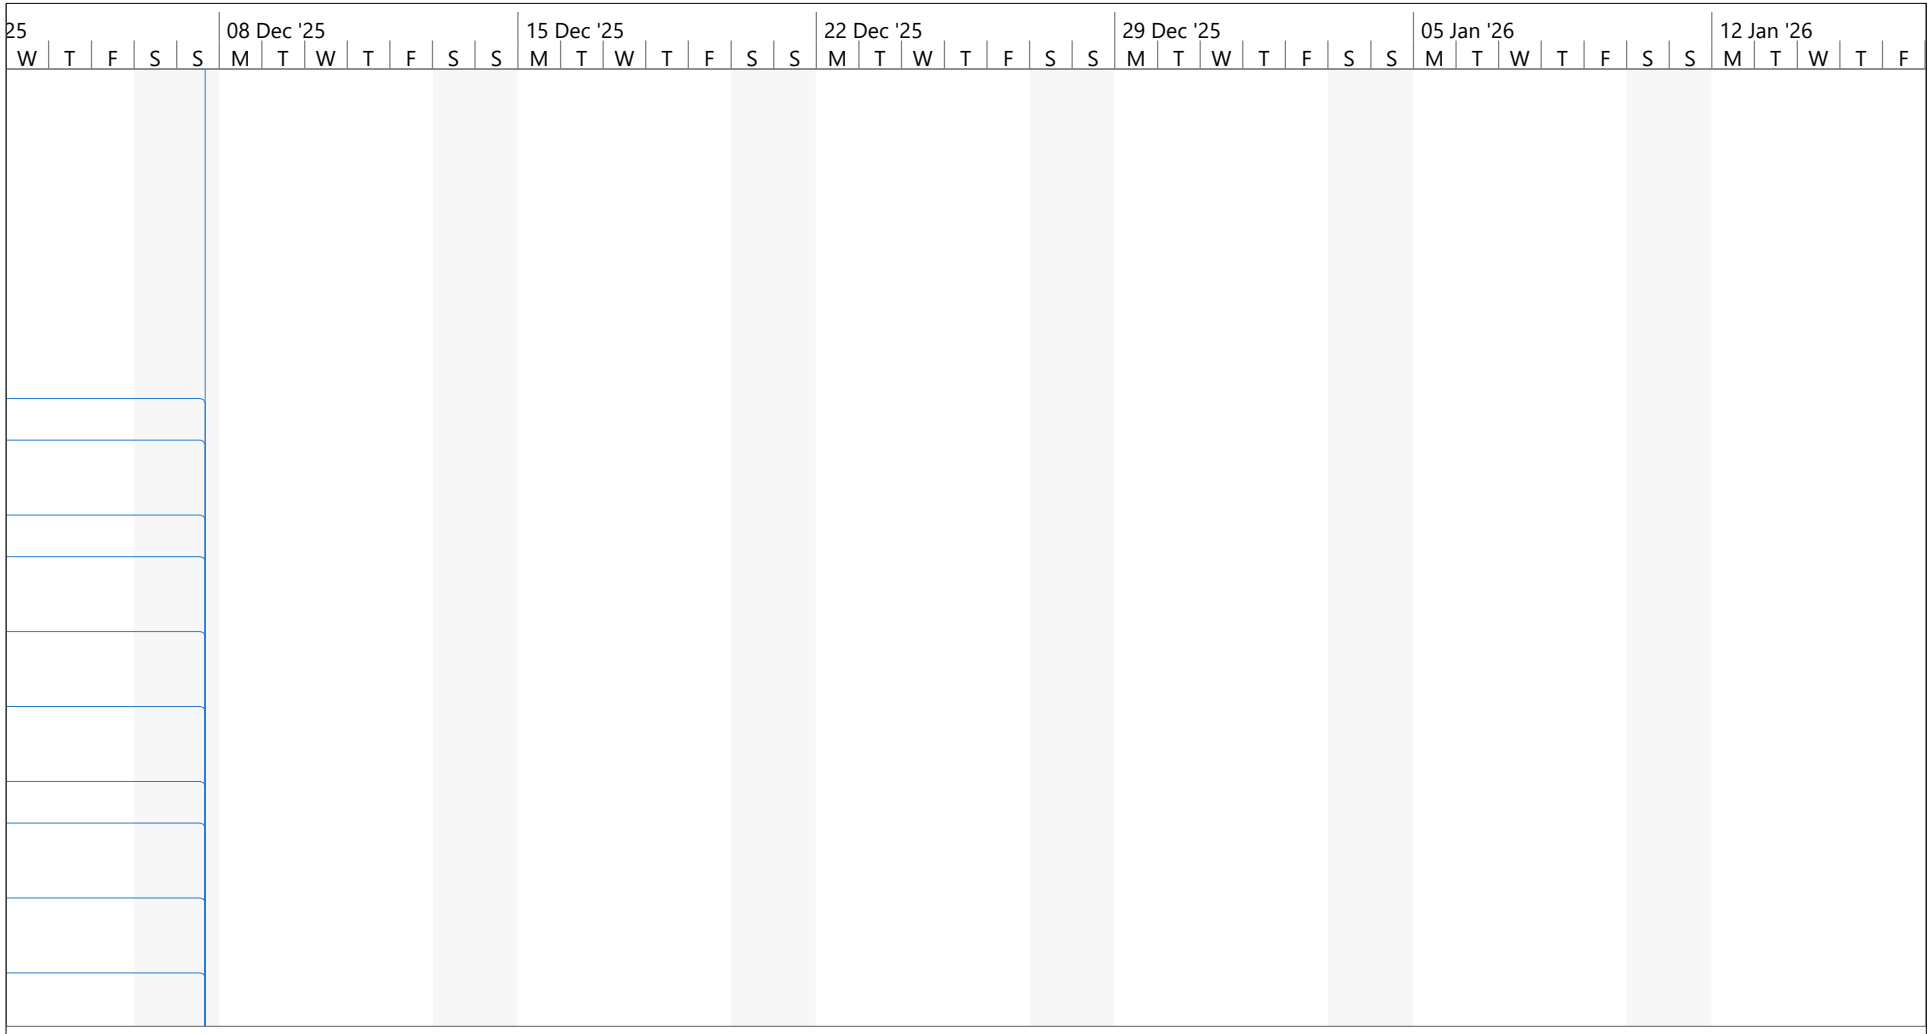

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

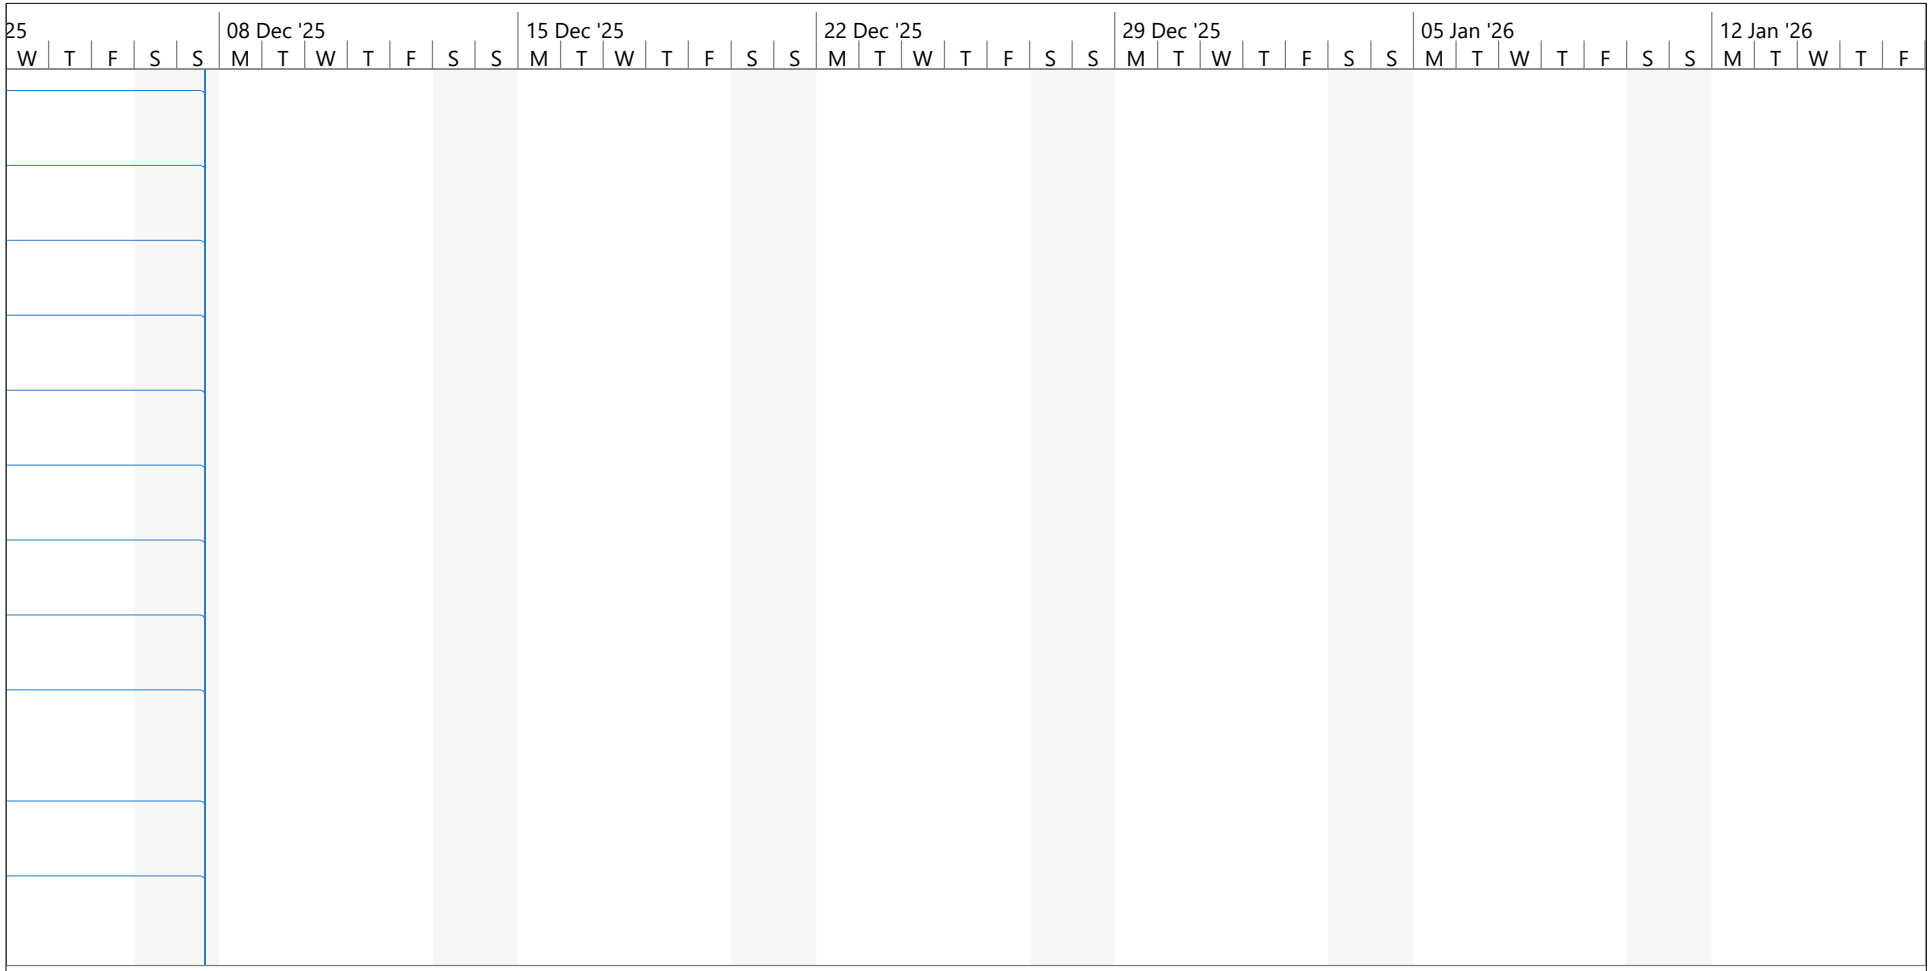

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

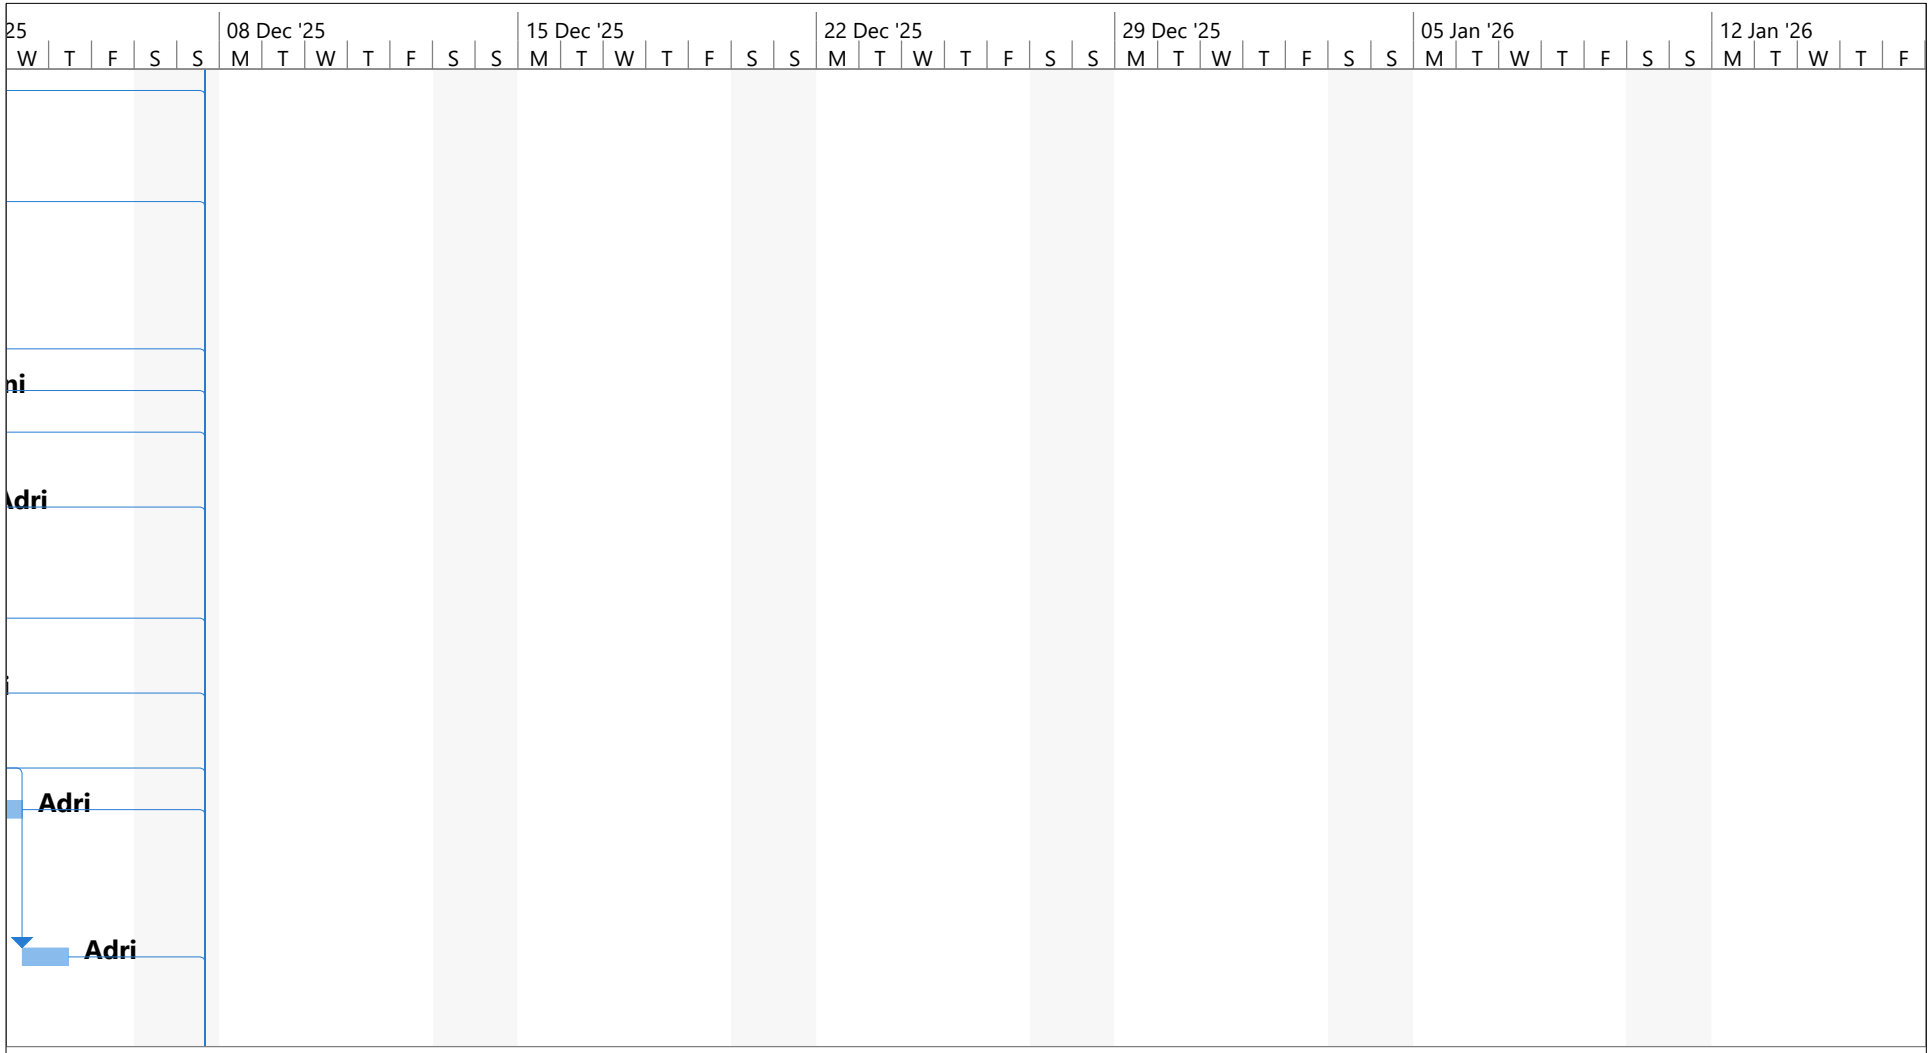

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

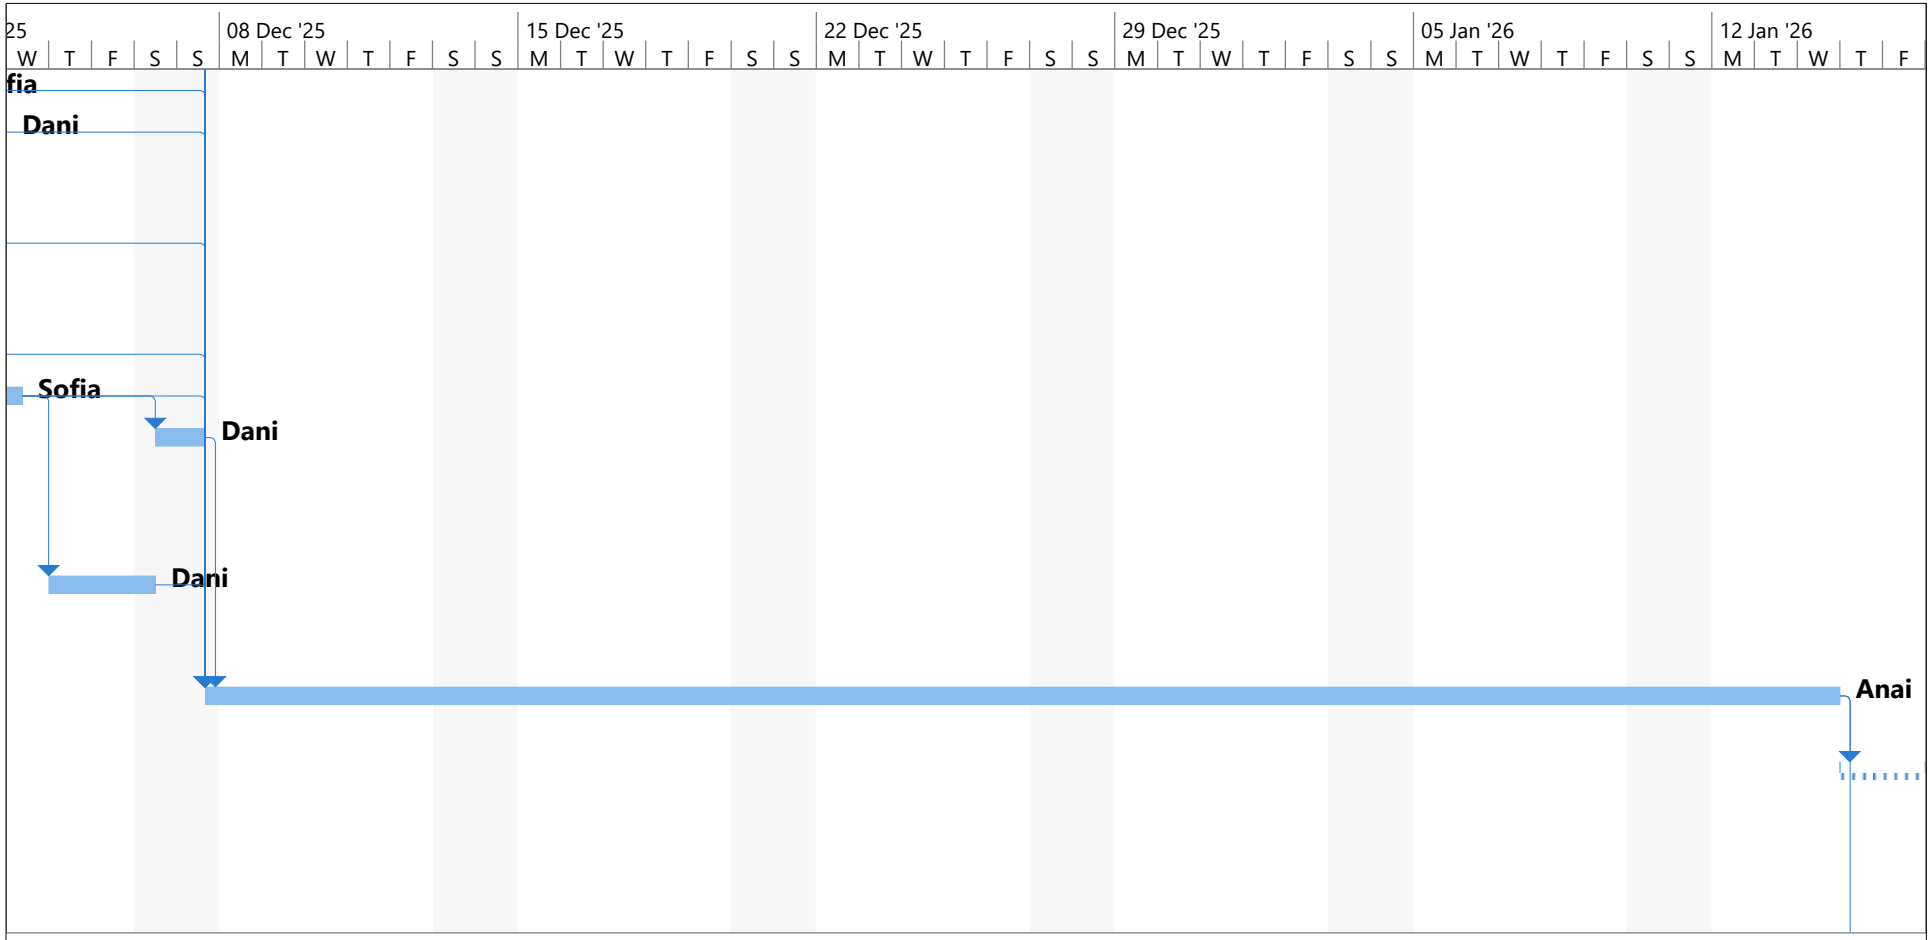

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

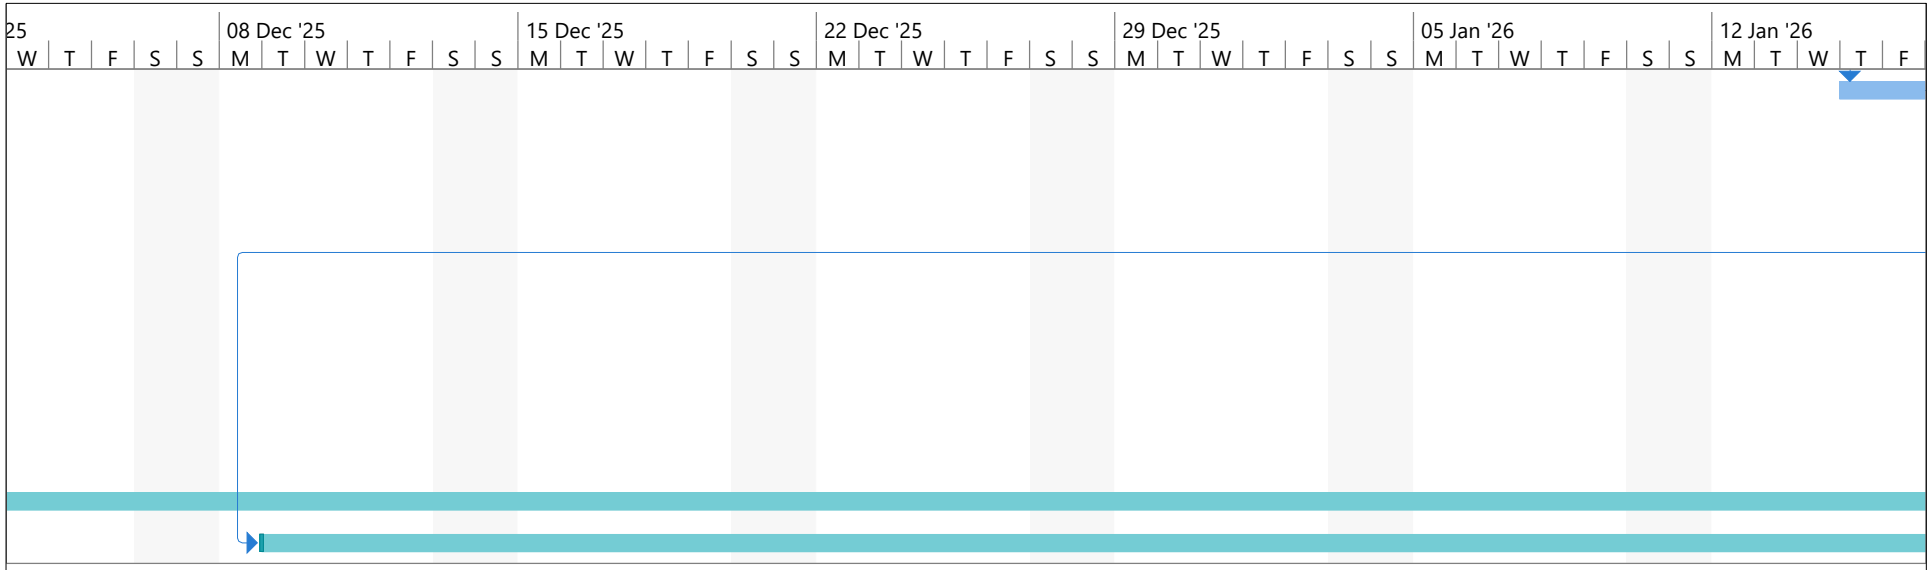

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

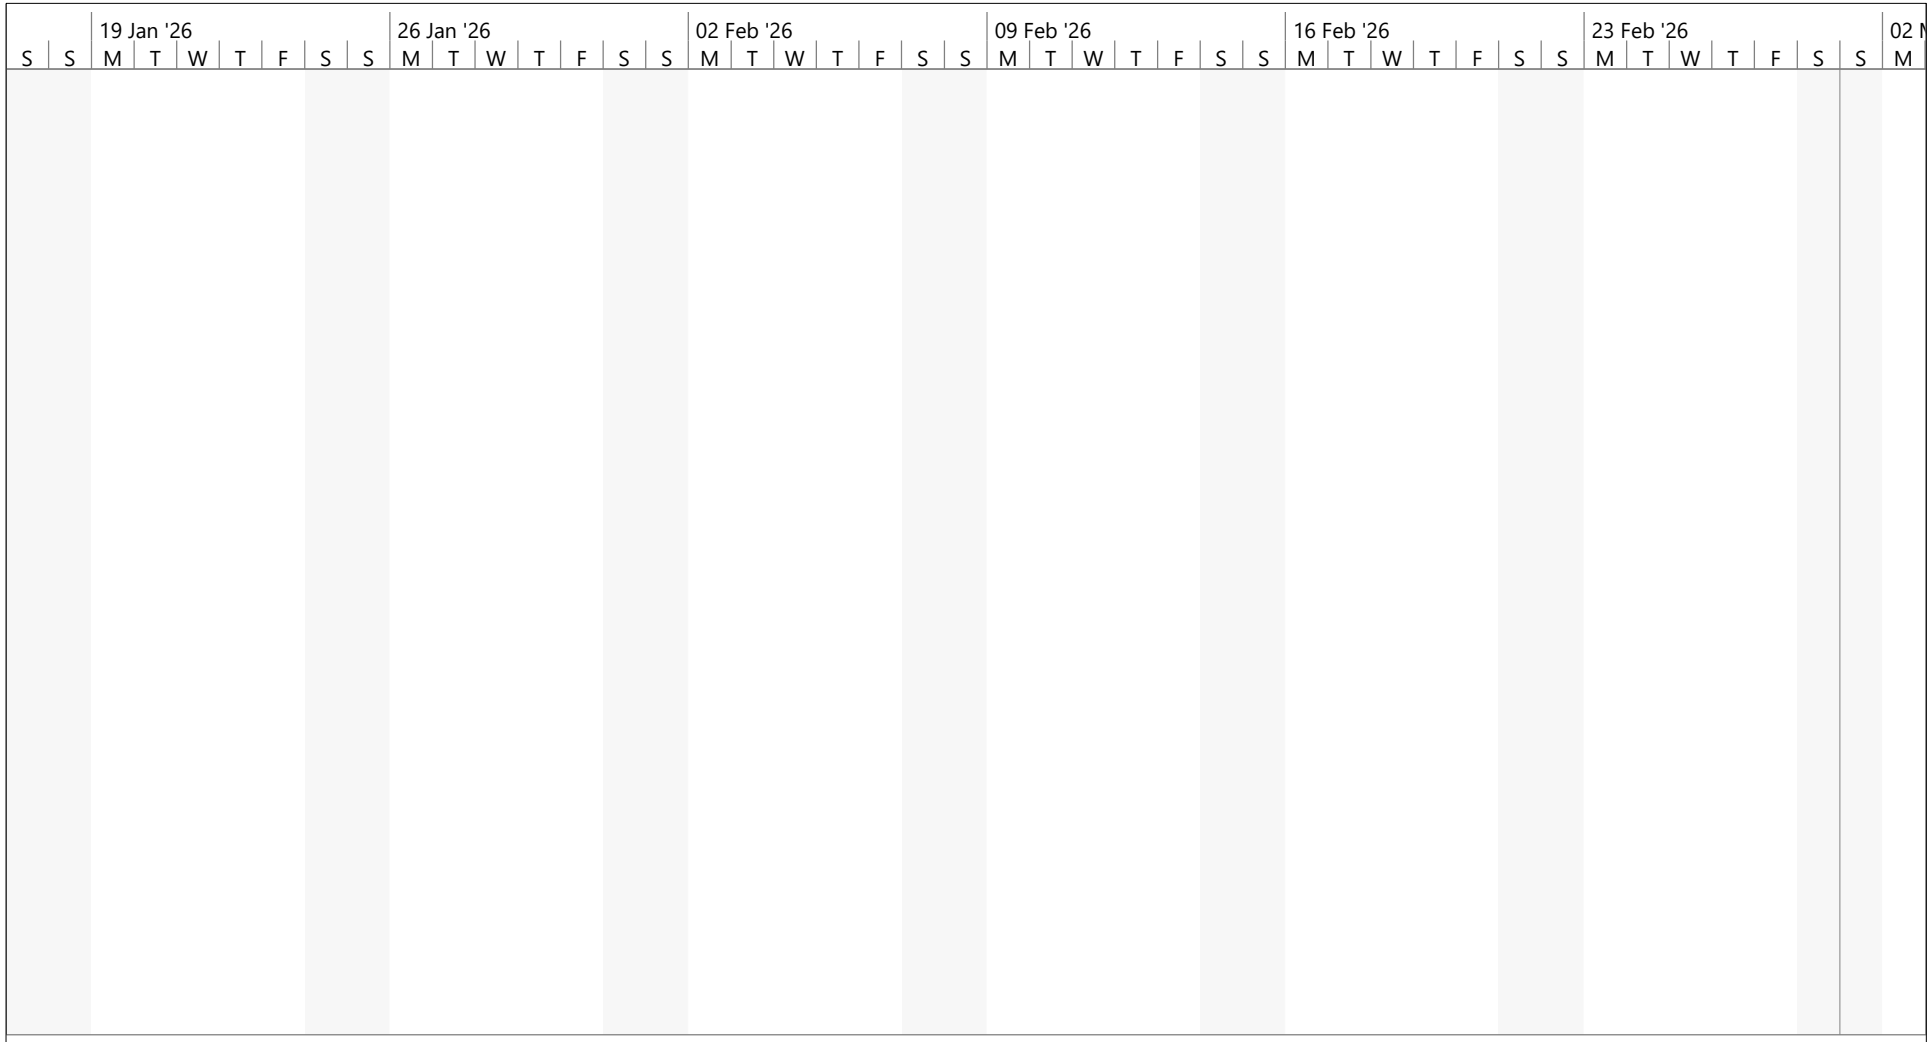

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

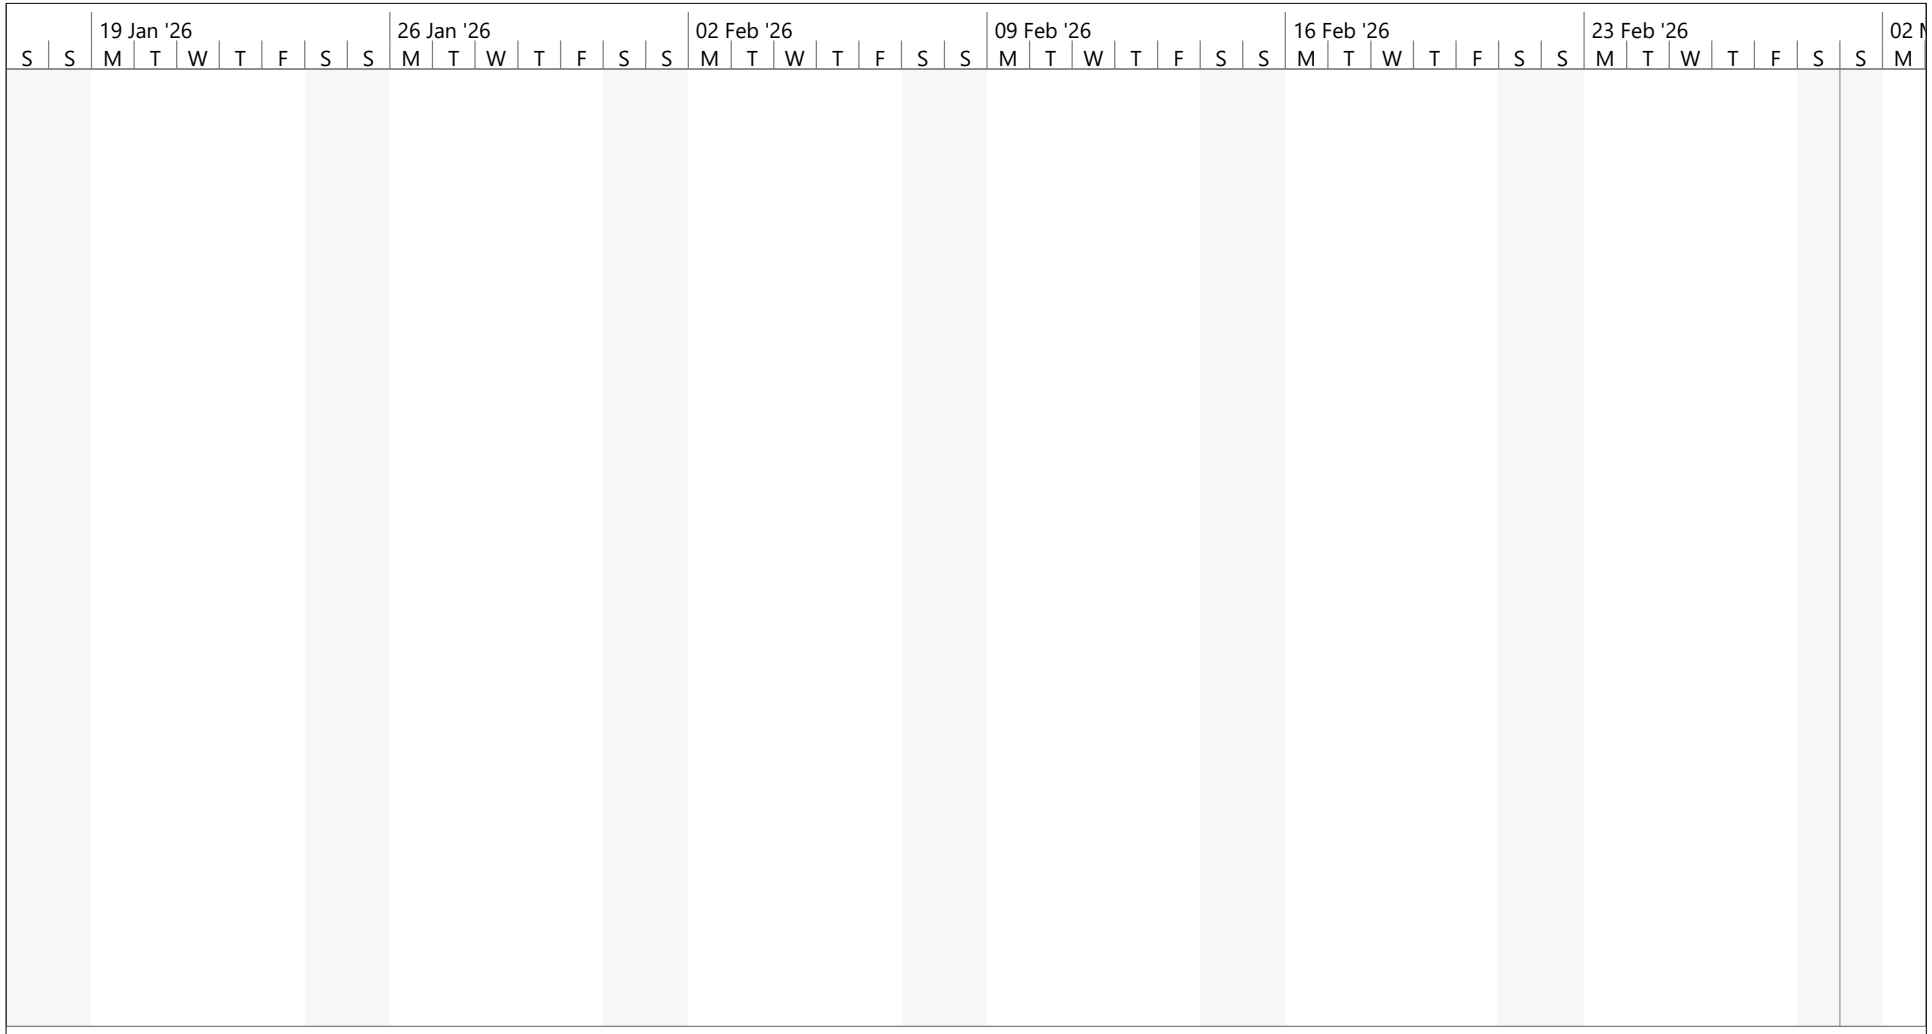

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

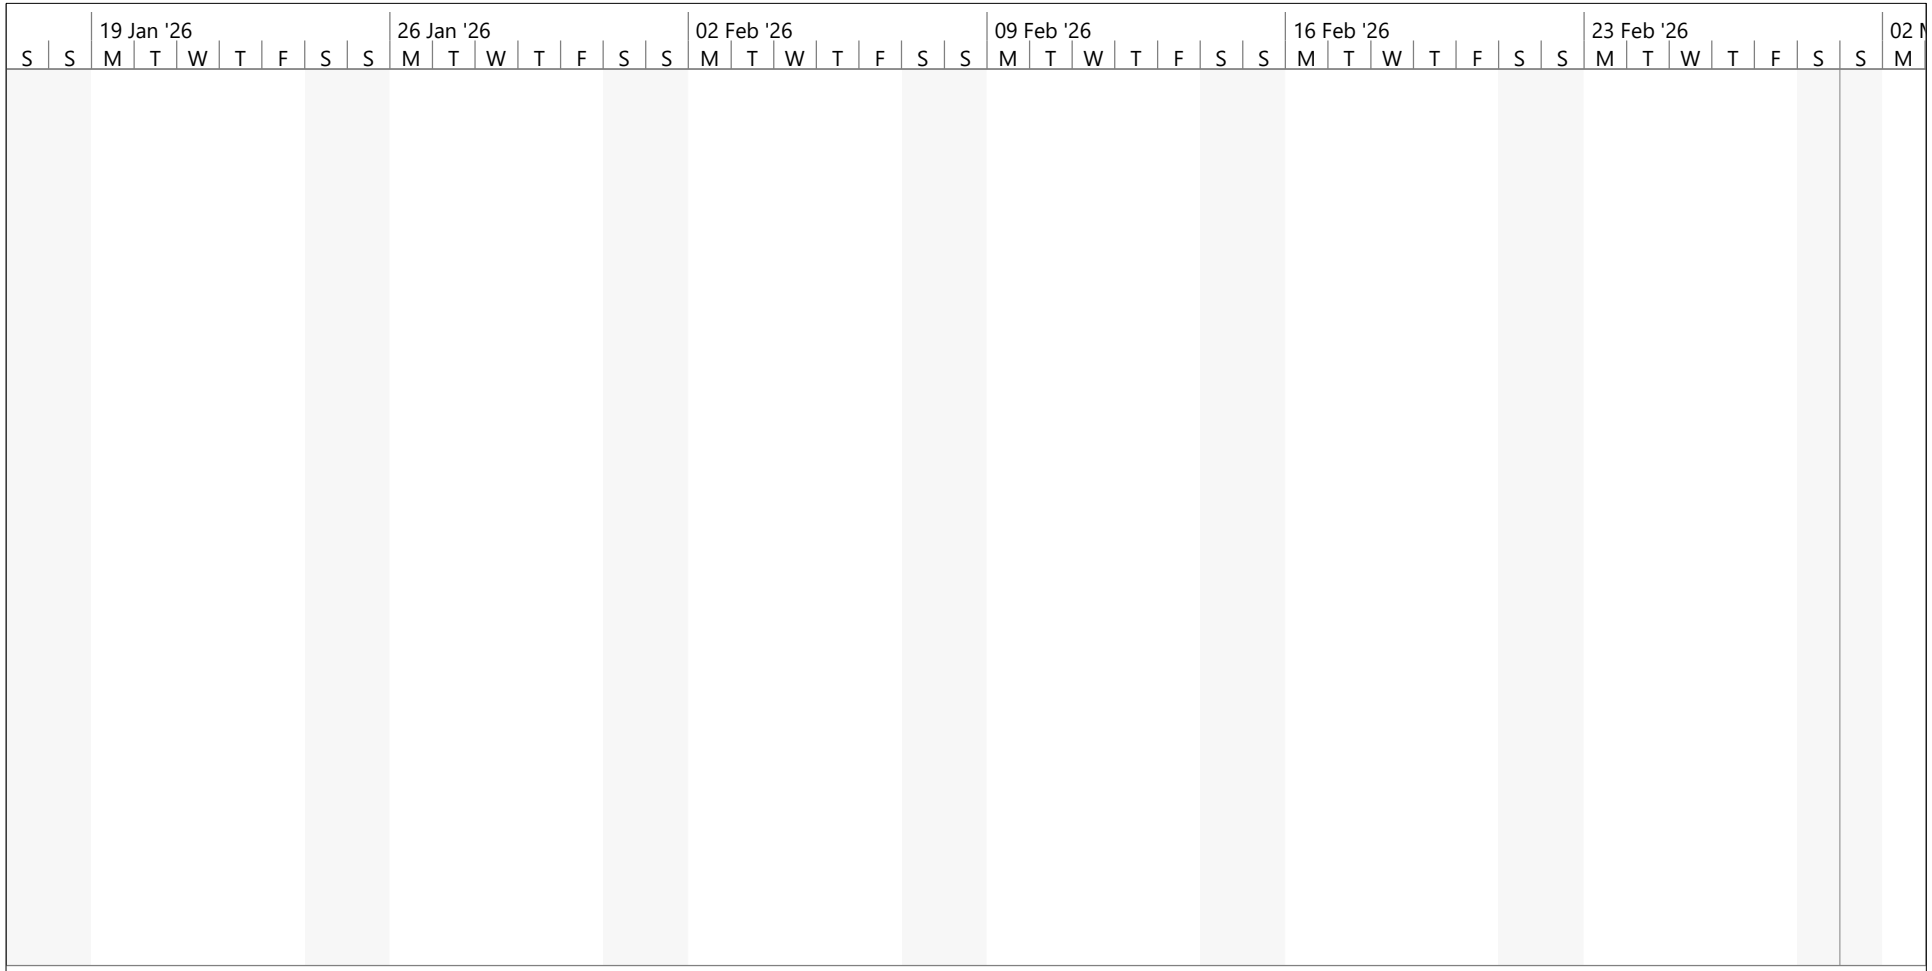

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

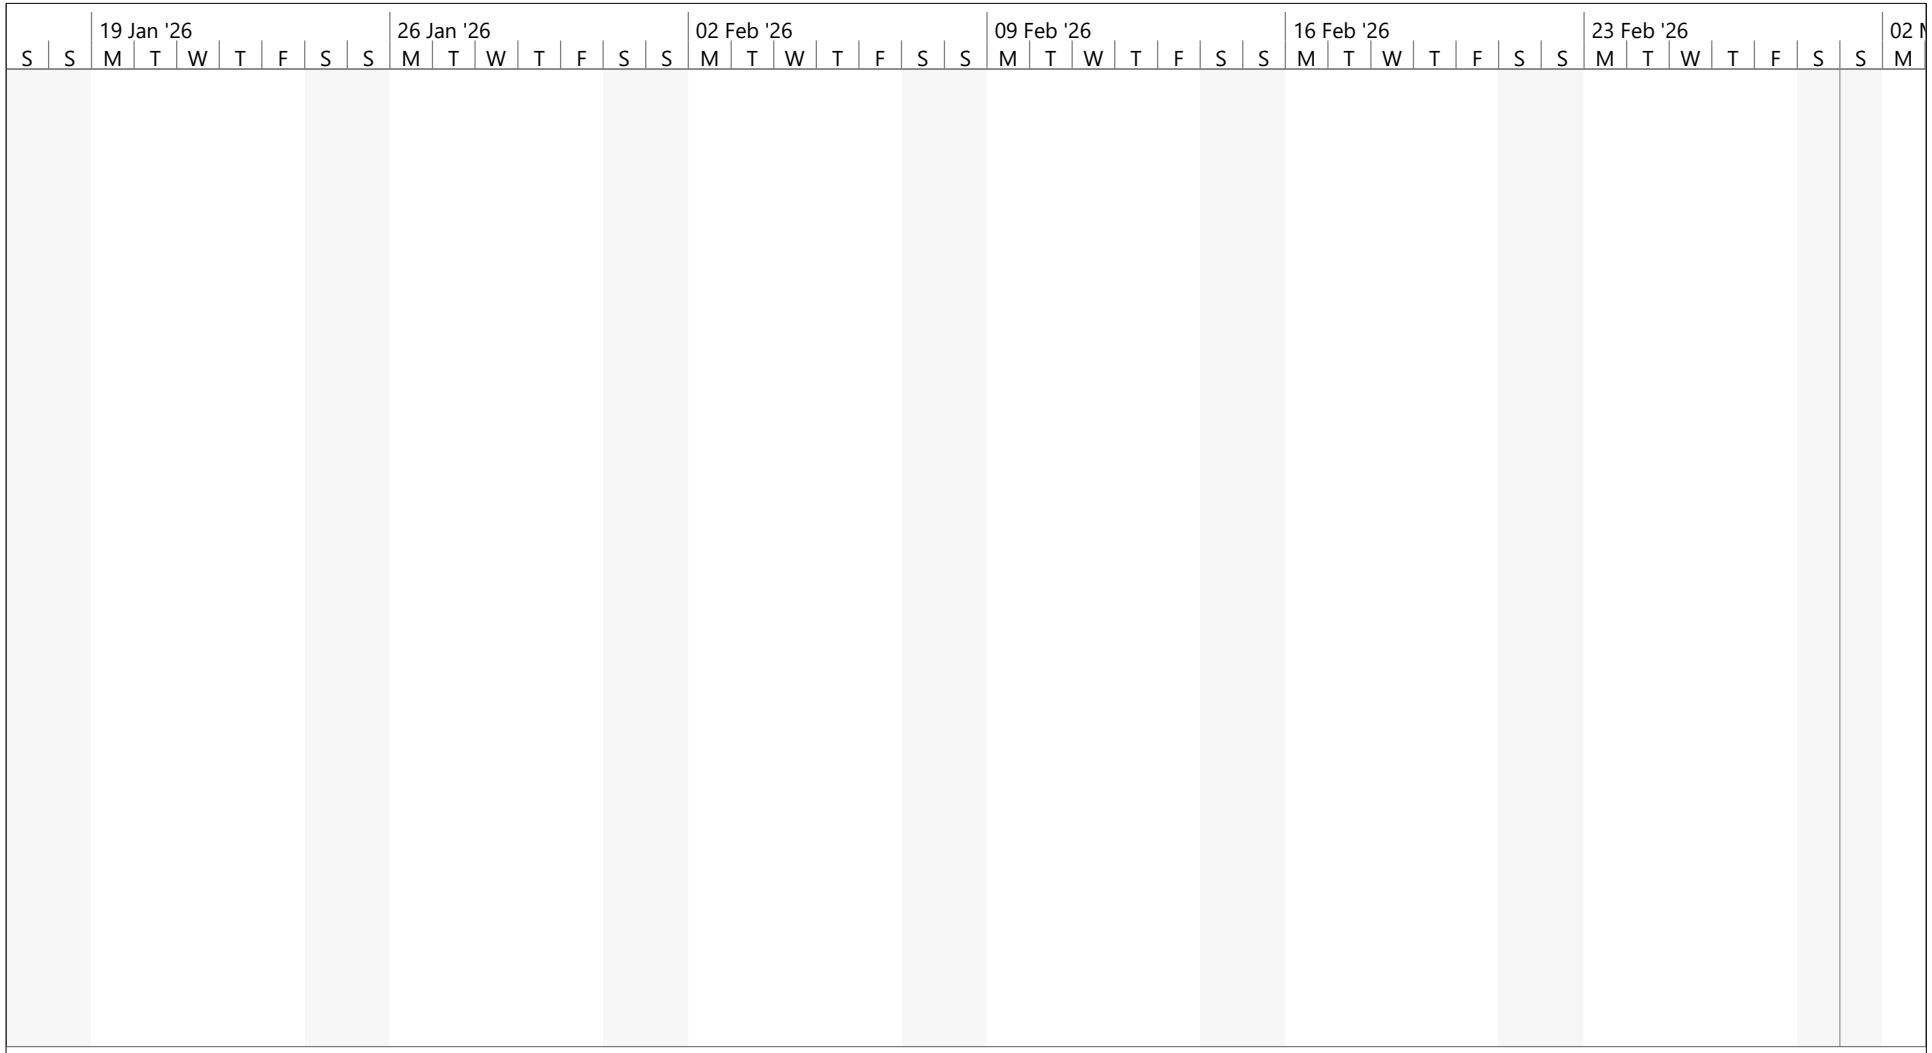

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

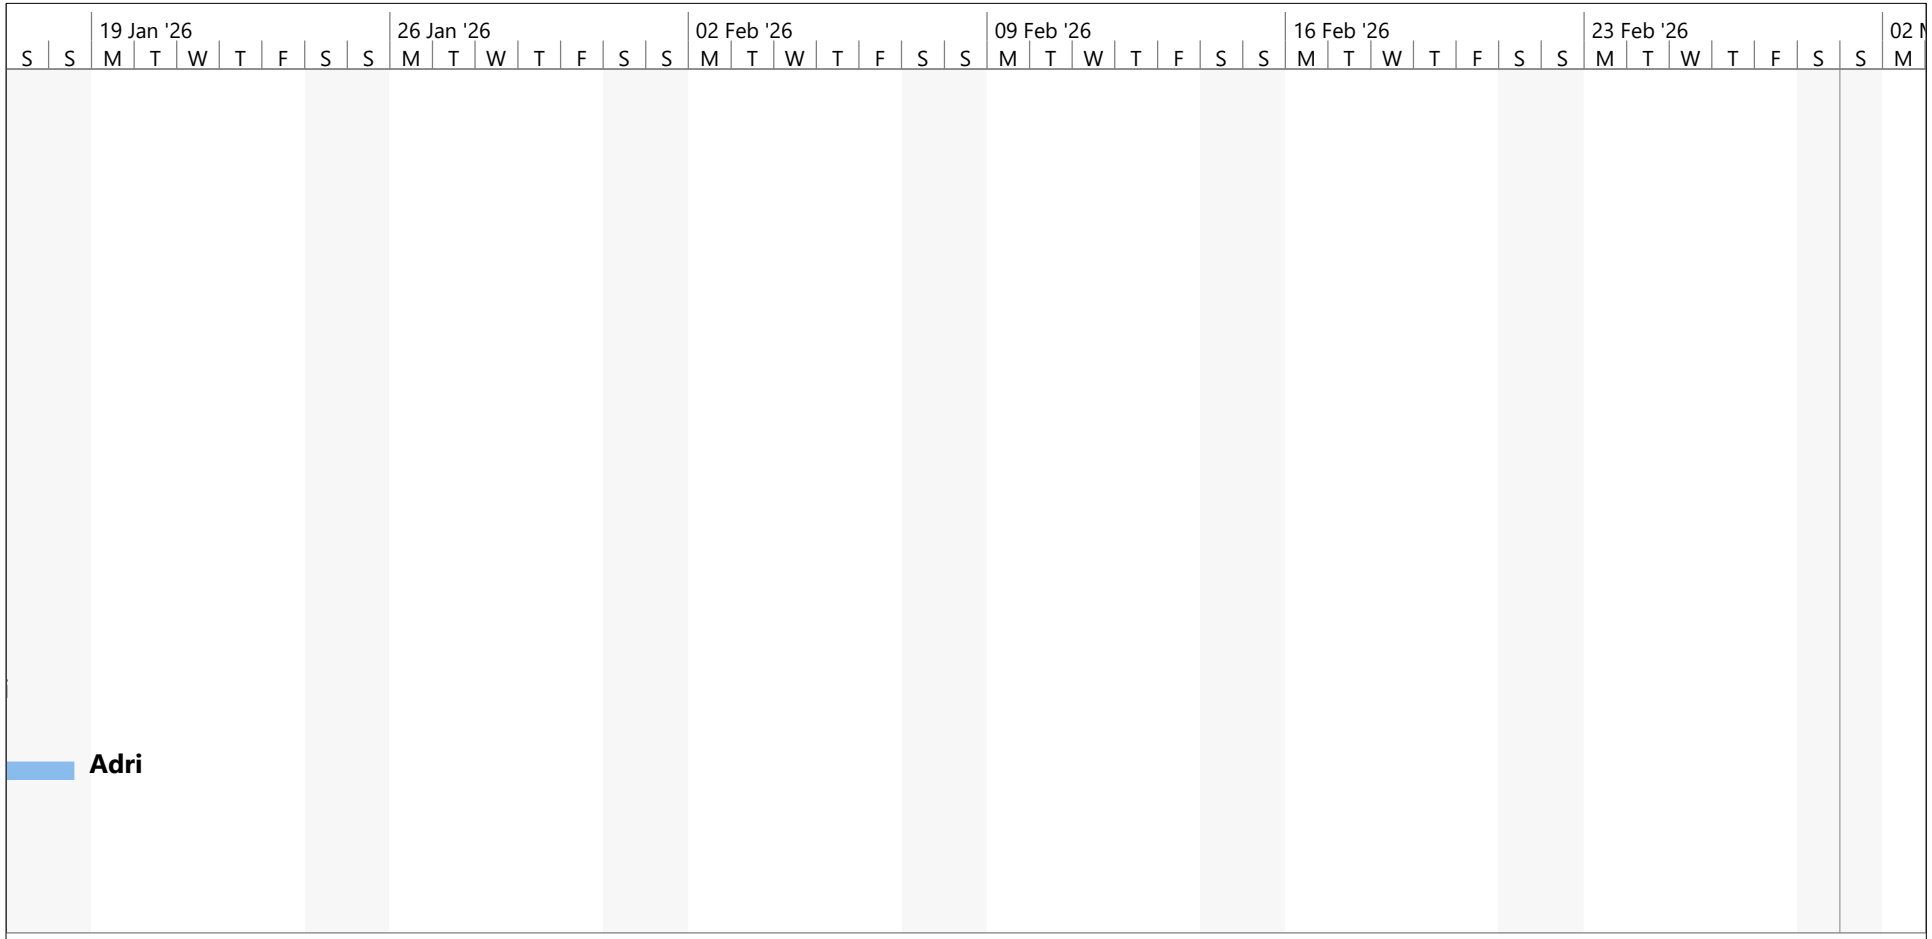

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

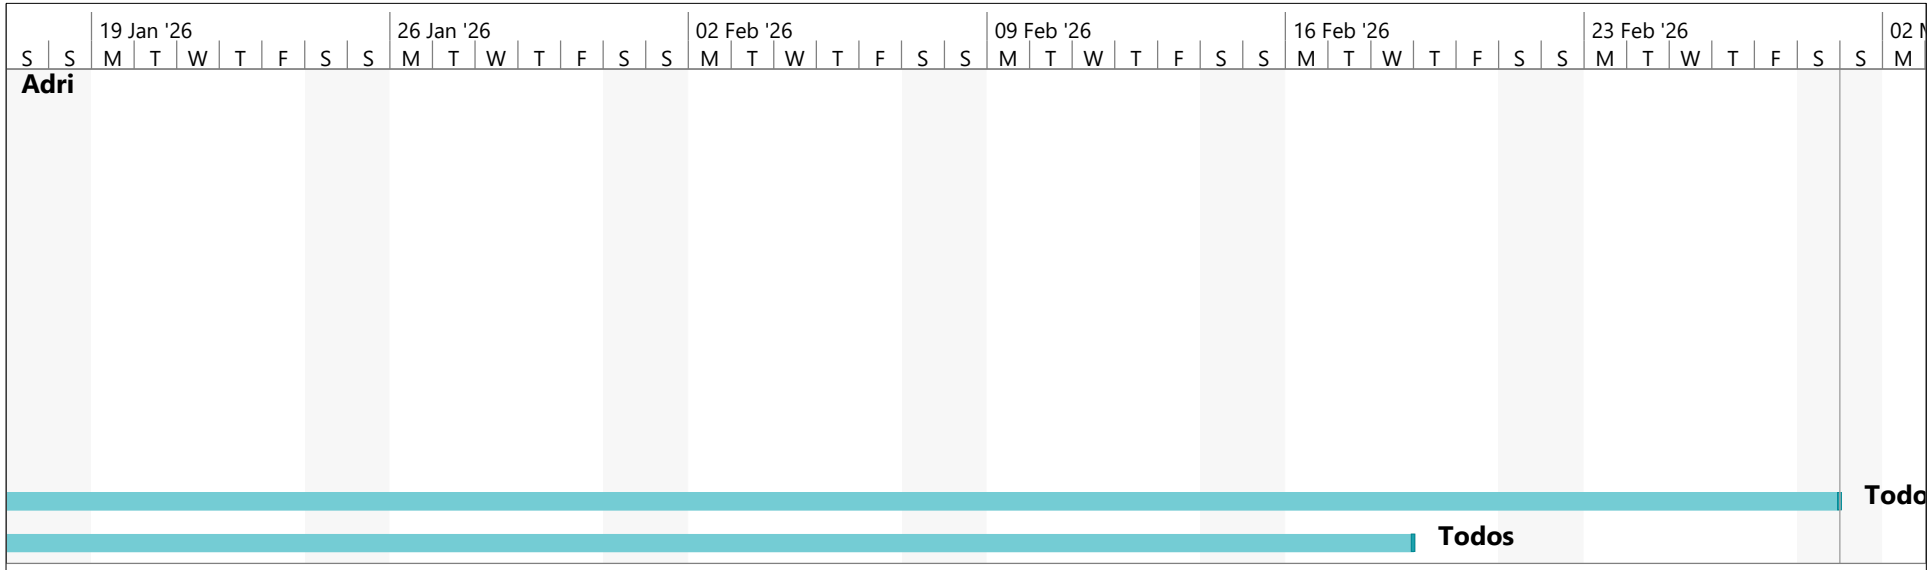

Project: Gantt_SmartMenu
Date: Fri 14/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
